

Works phasing

OPERATIONAL CENTER REPAIR - WORKS PHASING - ANNEX 1

PART 1 - GENERAL CONDITIONS

ADD- A02

FOR TENDERING
ADDENDUM A02 (2019-04-16)

ADD- A02

FORILLON NATIONAL PARK, GASPÉSIE, QUEBEC
1415

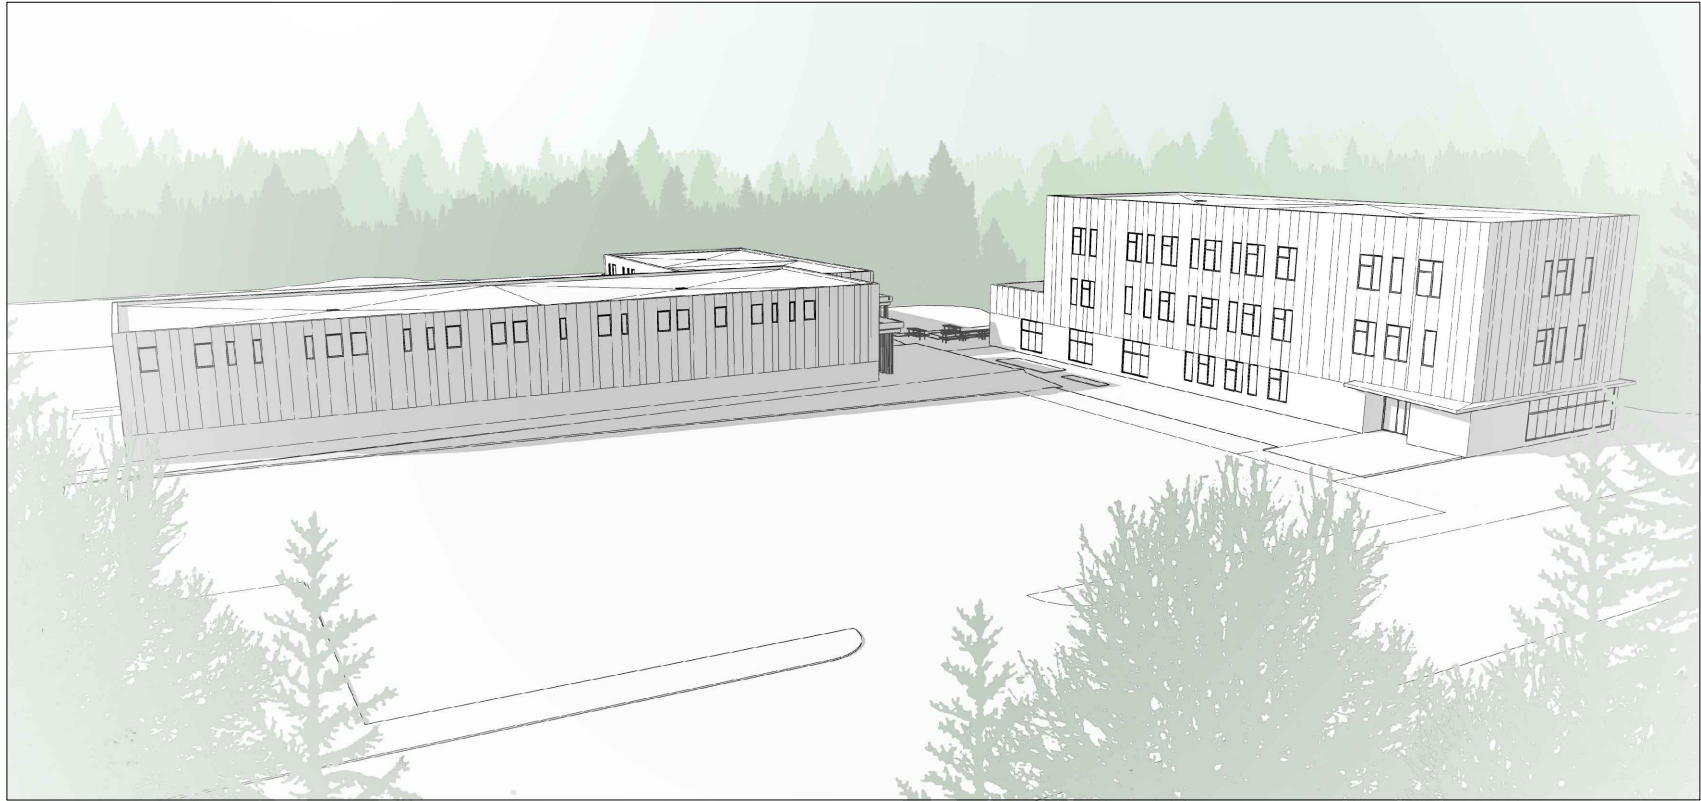


IMAGE FOR INFORMATION ONLY

LIST OF DRAWINGS

DRAWING	DRAWING TITLE
00	COVER PAGE
01	PHASE 1
02	PHASE 2
03	PHASE 3
04	PHASE 4
05	PHASE 5
06	PHASE 6
07	PHASE 7
08	PHASE 8
09	PHASE 9
10	PHASE 10
11	PHASE 11

ADD- A02

ADD- A02



2019-04-19



stgm

2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-626-8224



TETRA TECH



JBCA architectes

Project:
Operational Center Repair
& administrative center layout

Works phasing

Project number :

1415

Annex number :


ANNEX 1

Date :

2019-02-25

Drawing :

00/11

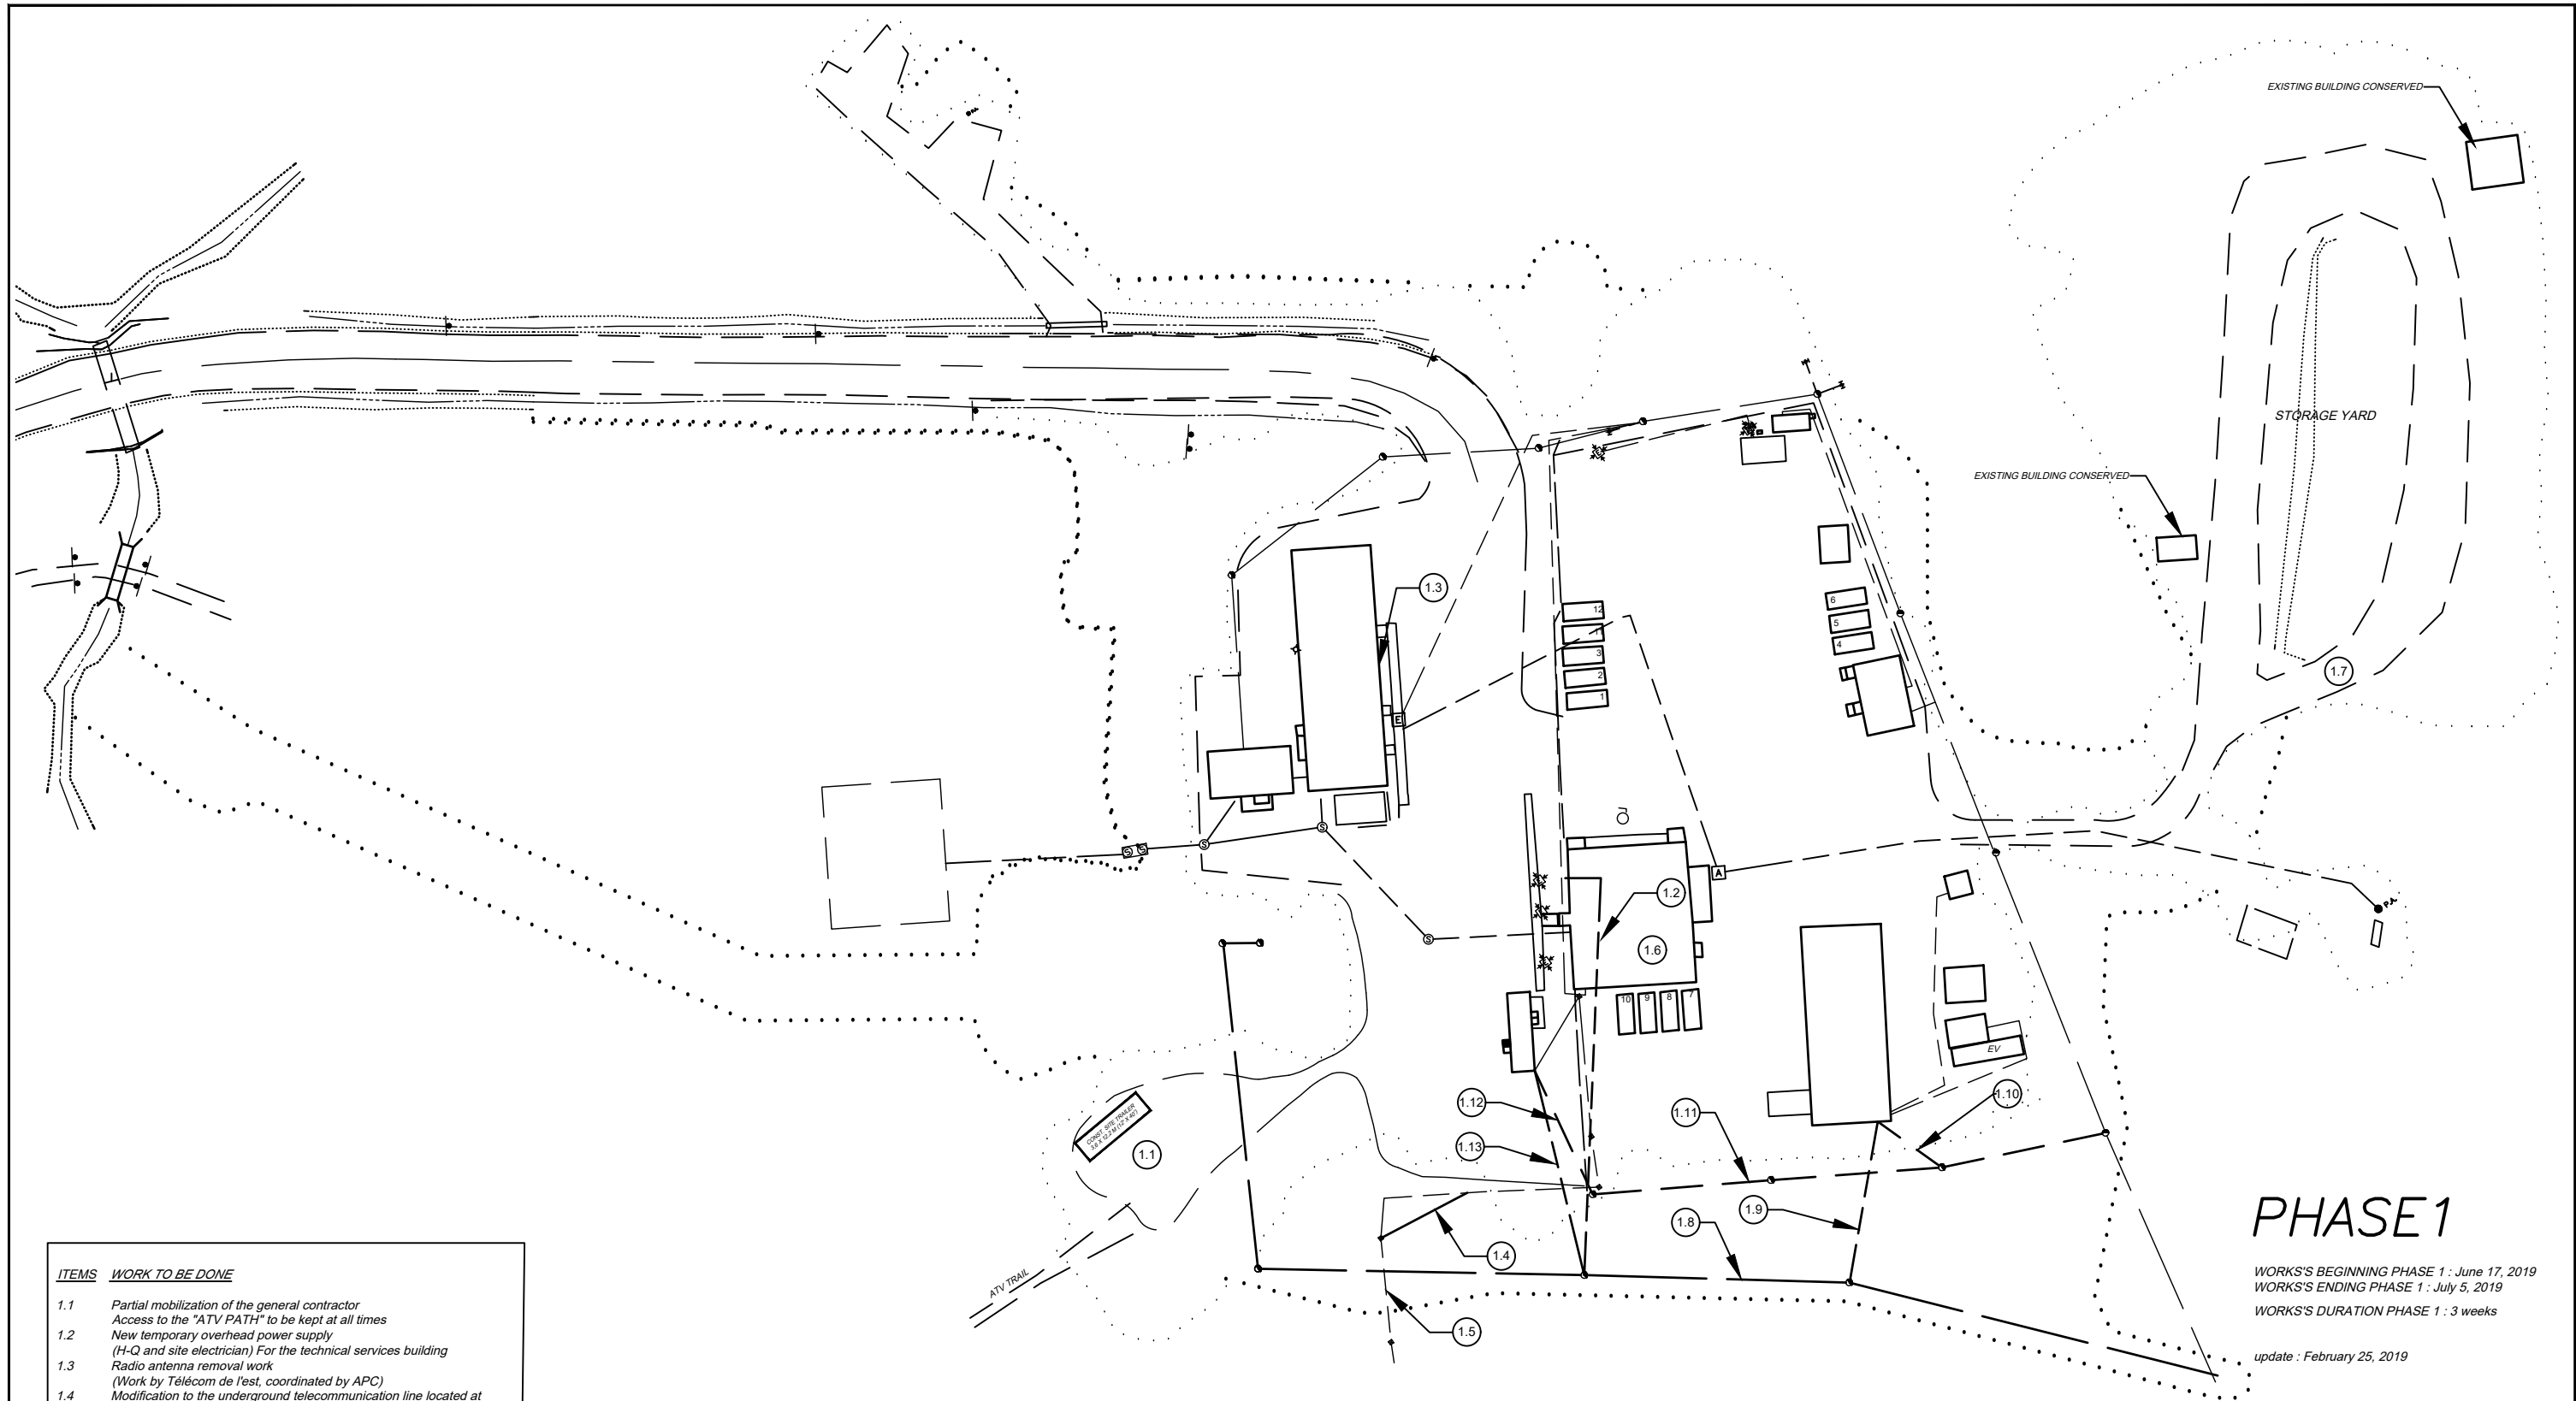

PHASE 1

WORKS'S BEGINNING PHASE 1 : June 17, 2019
WORKS'S ENDING PHASE 1 : July 5, 2019
WORKS'S DURATION PHASE 1 : 3 weeks

update : February 25, 2019

ITEMS	WORK TO BE DONE
1.1	Partial mobilization of the general contractor Access to the "ATV PATH" to be kept at all times
1.2	New temporary overhead power supply (H-Q and site electrician) For the technical services building
1.3	Radio antenna removal work (Work by Télécom de l'est, coordinated by APC)
1.4	Modification to the underground telecommunication line located at the "SOUTH-WEST" of the site
1.5	Existing underground telecommunication line to be preserved
1.6	Wi-Fi link of the gas station to be maintained in the technical services building
1.7	Site preparation on a section of the storage yard for container installation
1.8	New overhead power line
1.9	New temporary overhead power supply for the ATCO building
1.10	Existing power supply to be removed
1.11	Existing power line to be removed
1.12	Removal of the existing overhead power supply to the trailer "Projects"
1.13	New temporary overhead power supply for the "Projects" trailer



2019-04-19



stgm

2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-626-8224



TETRA TECH



architectes

Project:
Operational Center Repair
& administrative center layout

Works phasing

Project number :

1415

Annex number :


ANNEX 1


Date :

2019-02-25

Drawing :

01/11

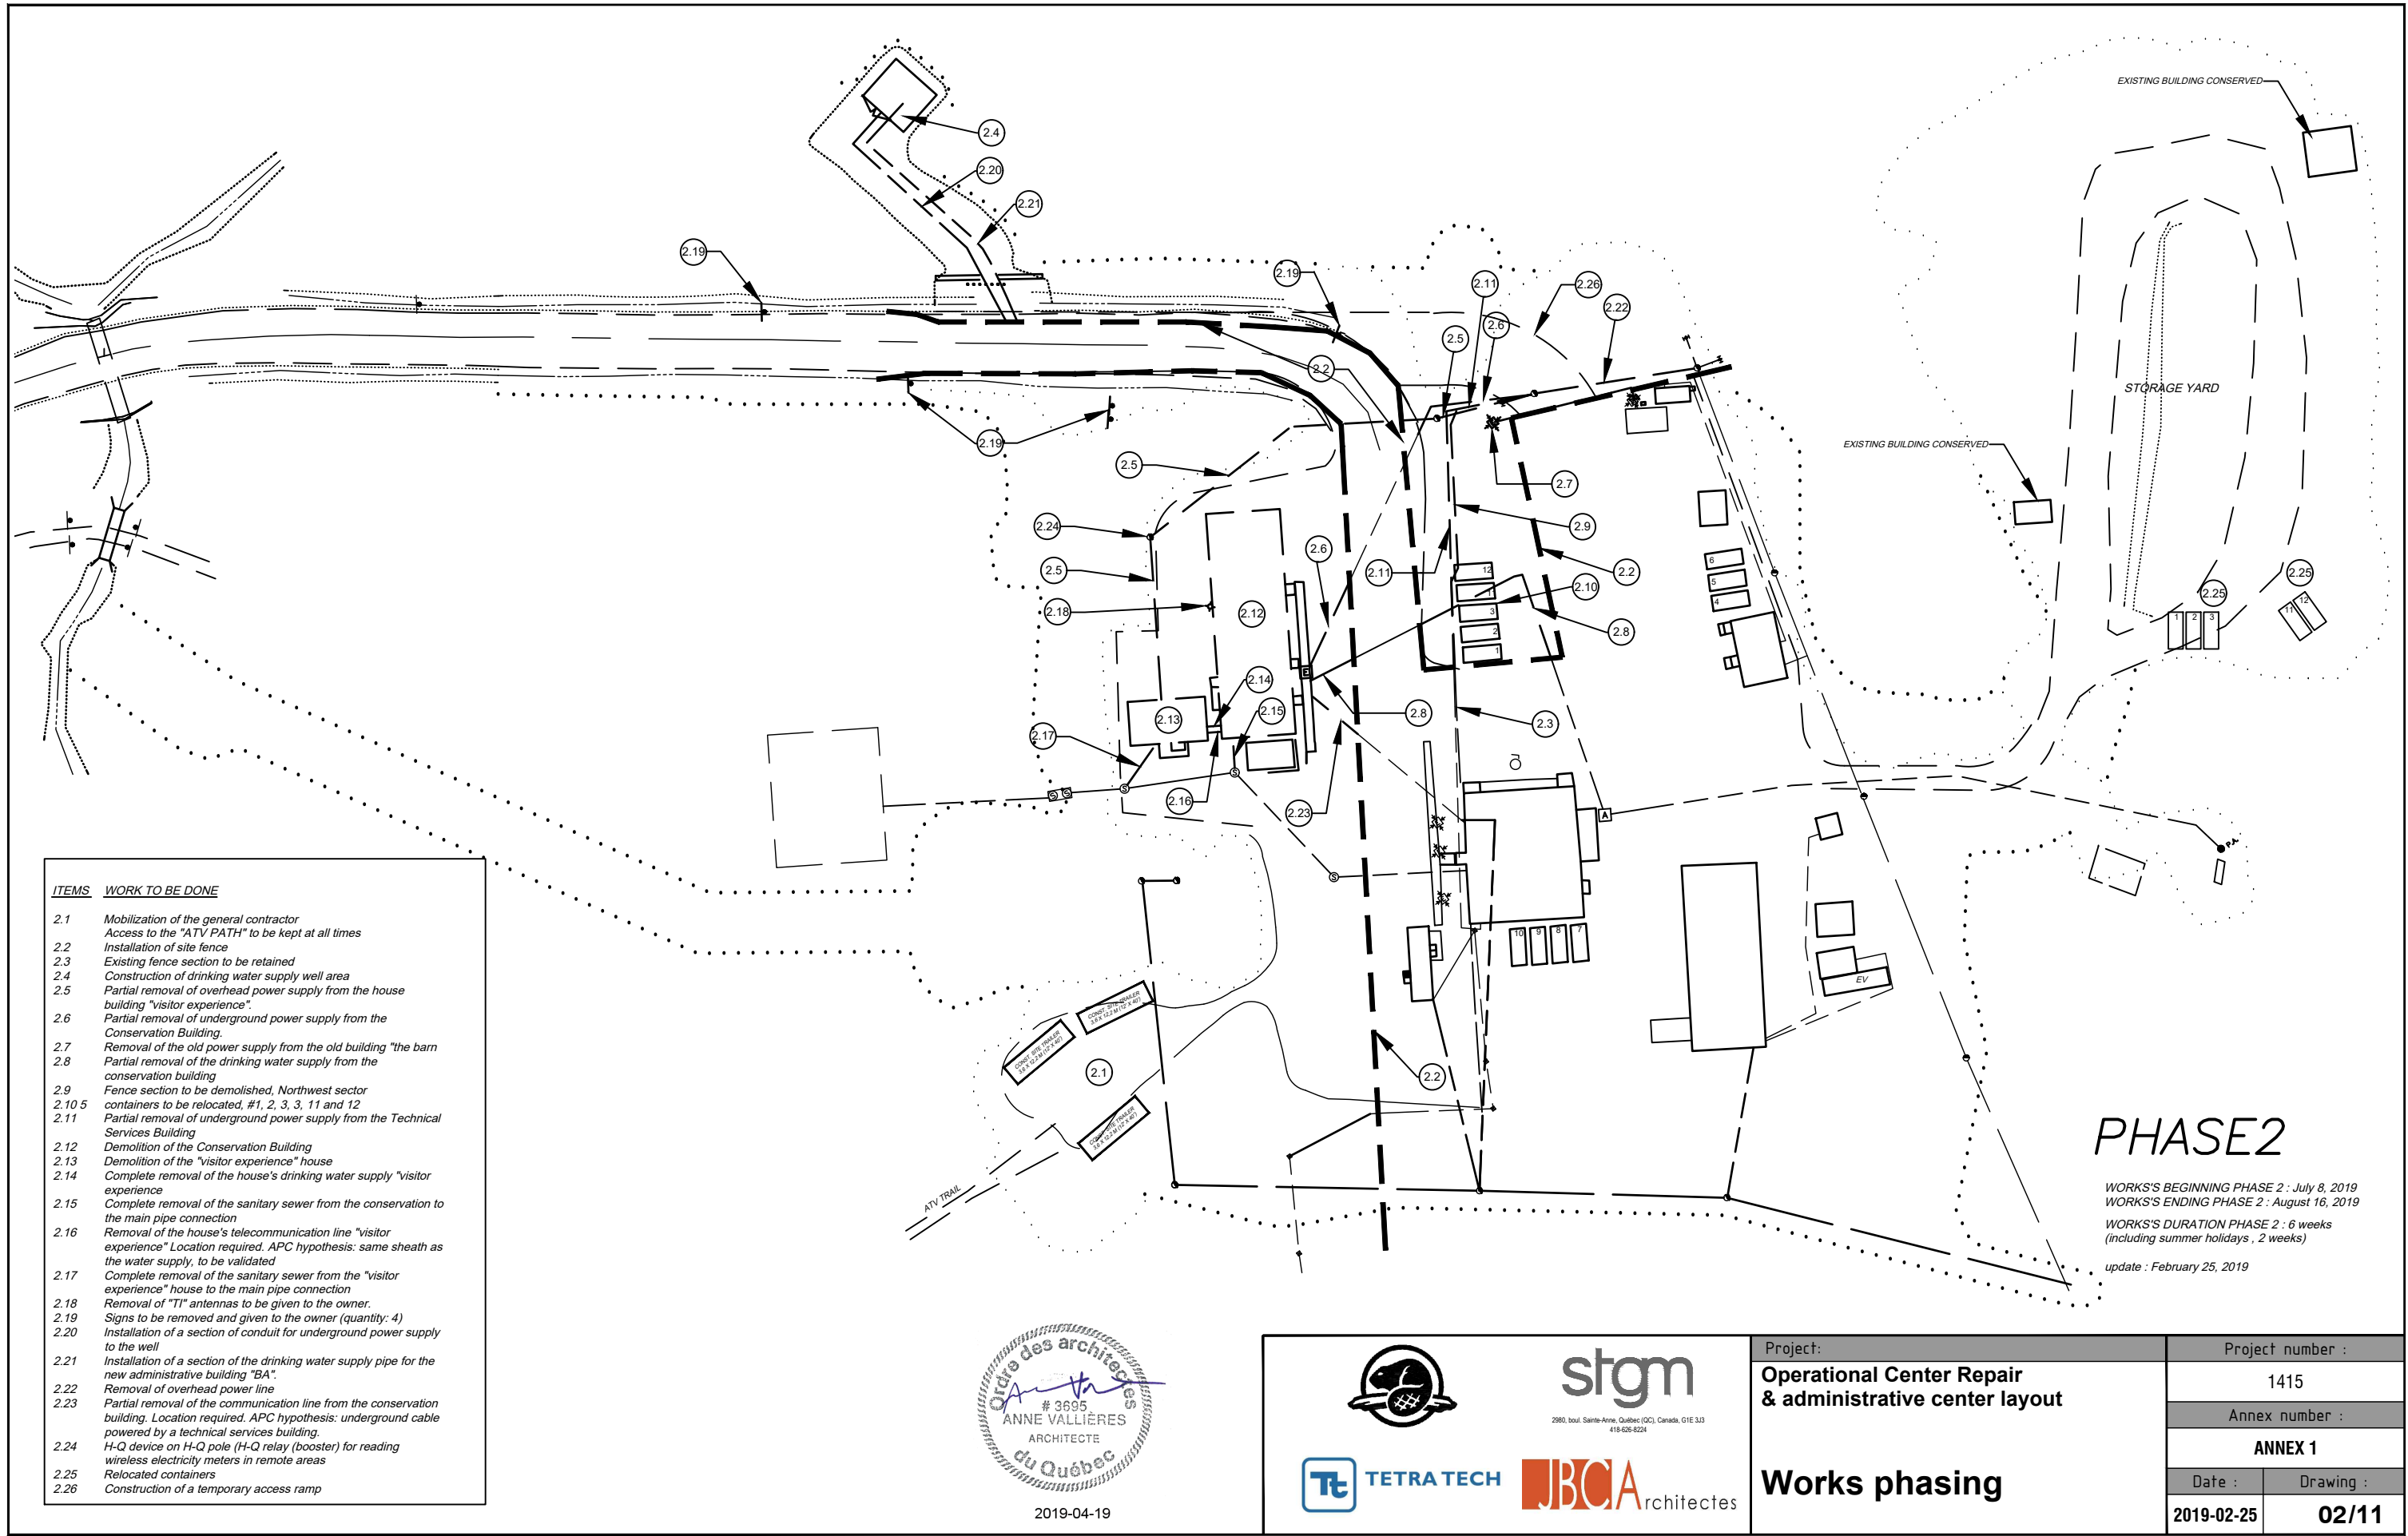

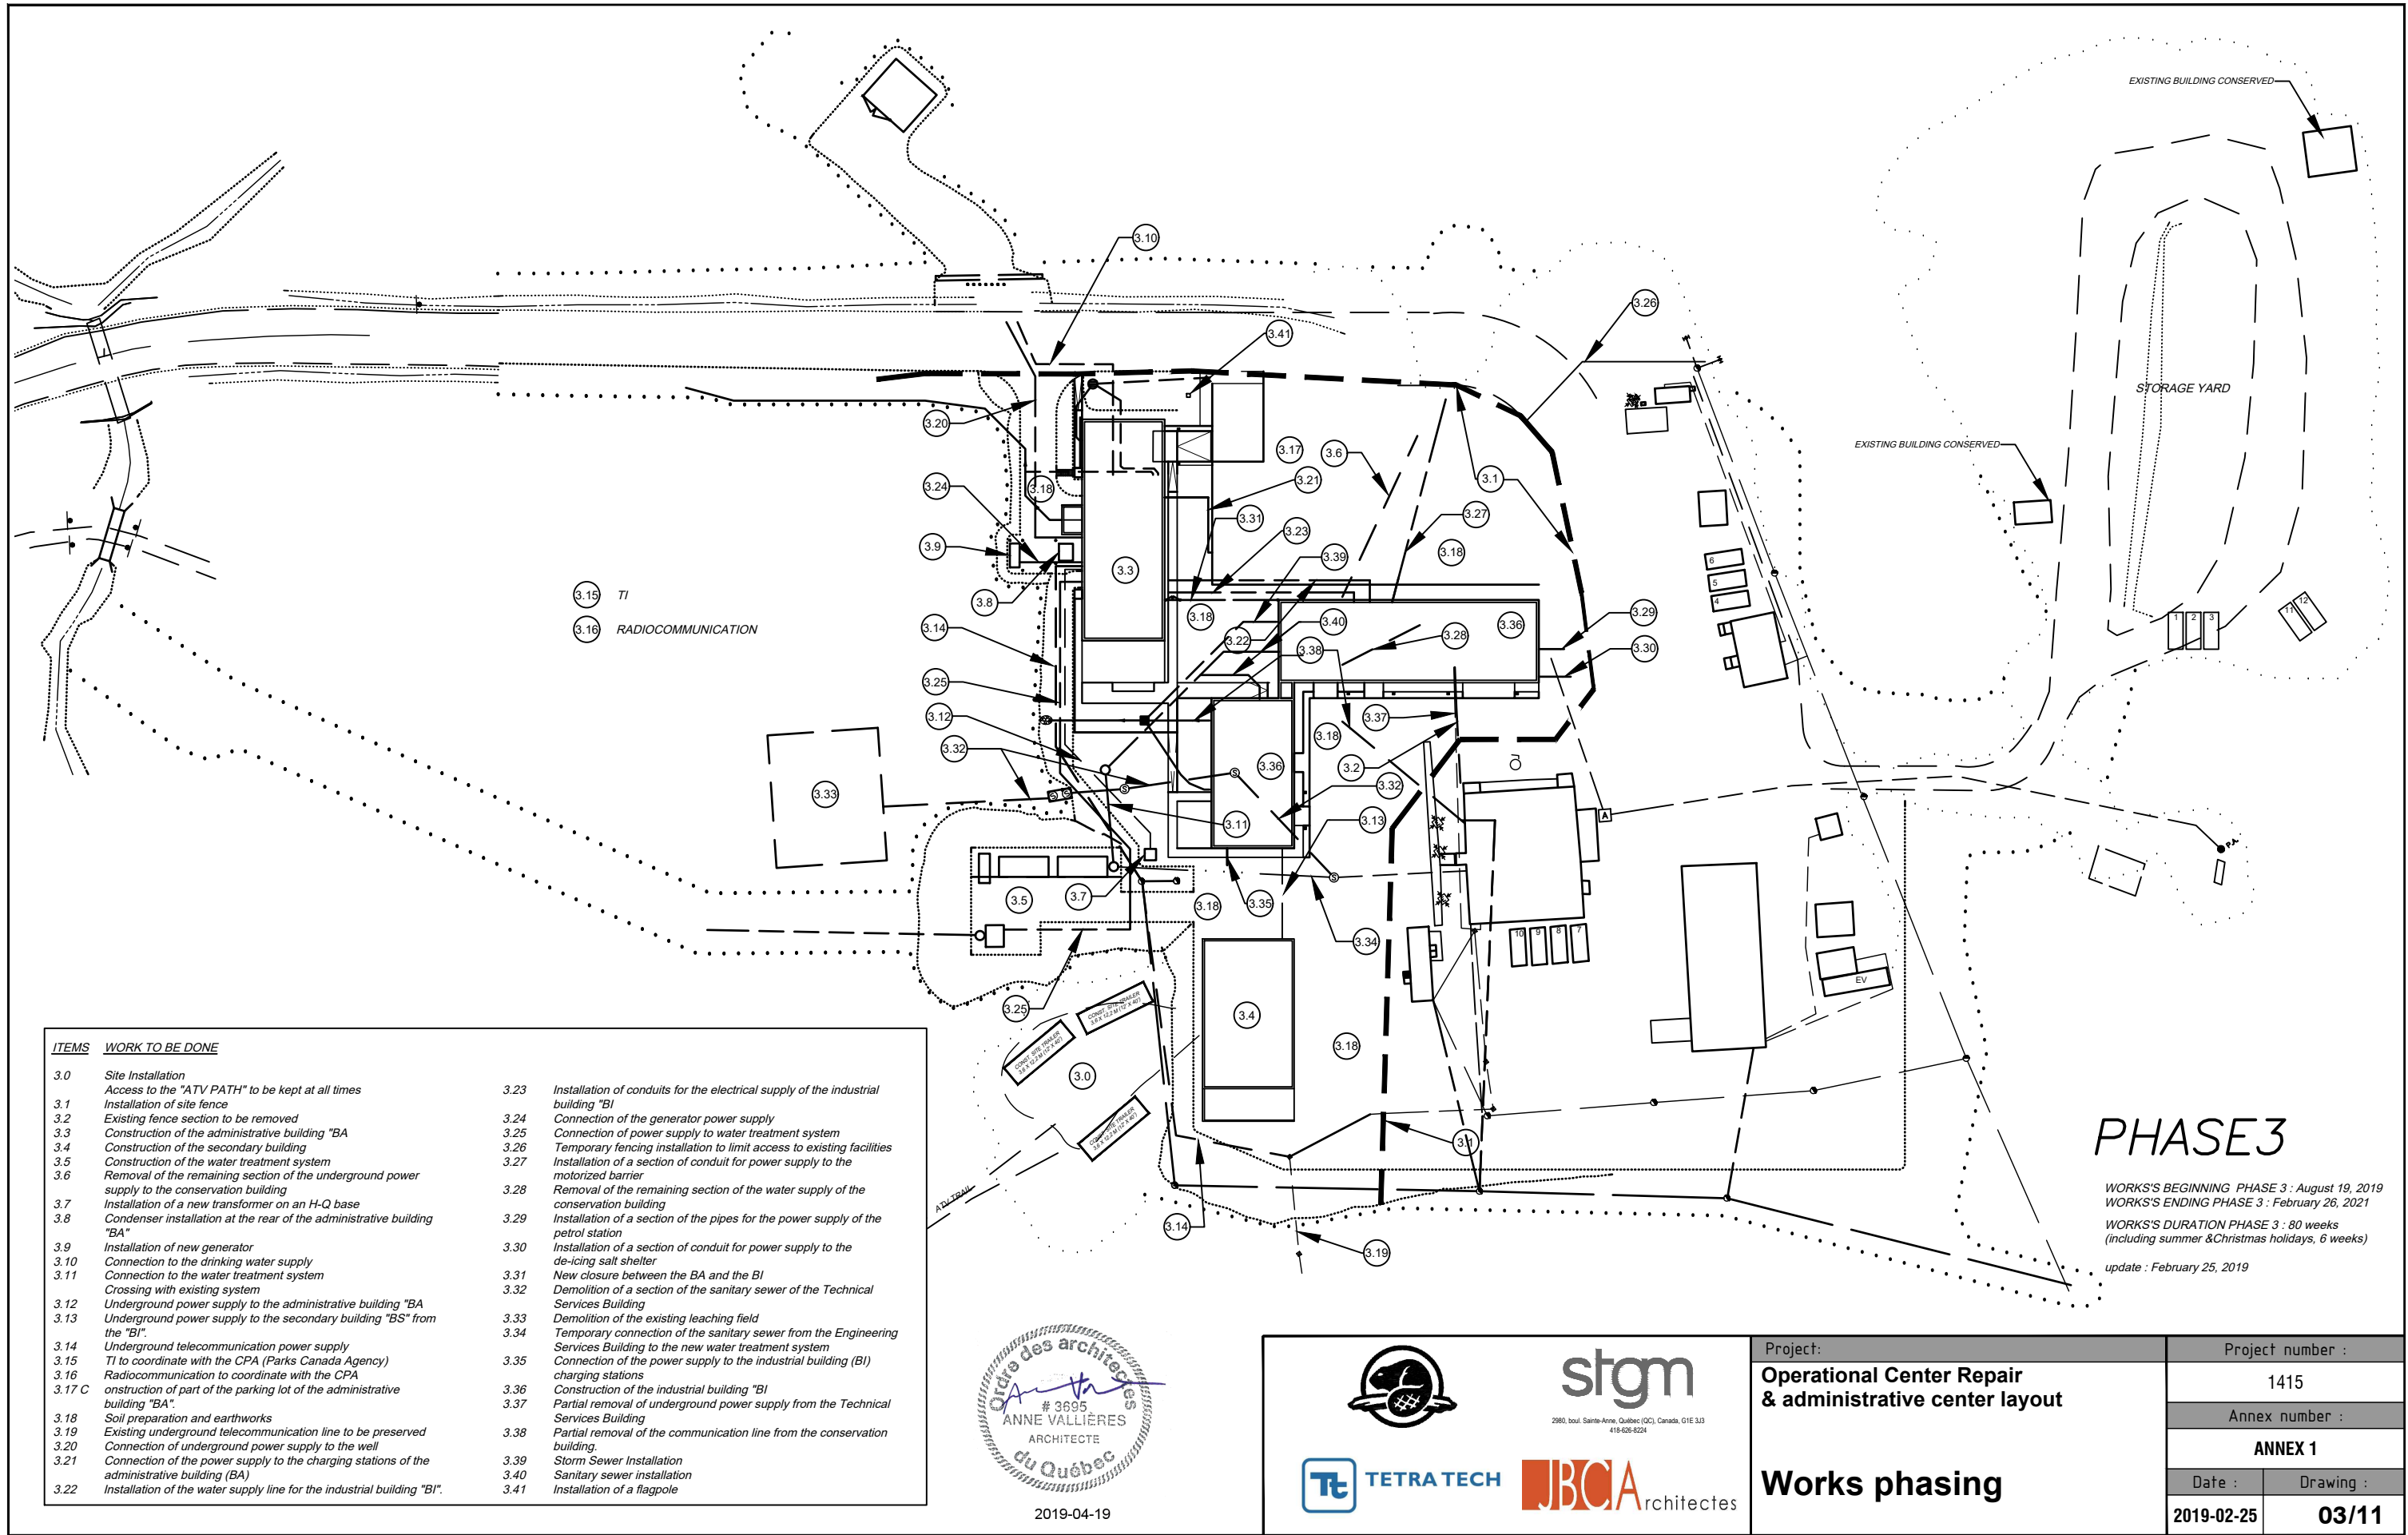

PHASE3

WORKS'S BEGINNING PHASE 3 : August 19, 2019
WORKS'S ENDING PHASE 3 : February 26, 2021
WORKS'S DURATION PHASE 3 : 80 weeks
(including summer & Christmas holidays, 6 weeks)
update : February 25, 2019

ITEMS	WORK TO BE DONE
3.0	Site Installation Access to the "ATV PATH" to be kept at all times
3.1	Installation of site fence
3.2	Existing fence section to be removed
3.3	Construction of the administrative building "BA"
3.4	Construction of the secondary building
3.5	Construction of the water treatment system
3.6	Removal of the remaining section of the underground power supply to the conservation building
3.7	Installation of a new transformer on an H-Q base
3.8	Condenser installation at the rear of the administrative building "BA"
3.9	Installation of new generator
3.10	Connection to the drinking water supply
3.11	Connection to the water treatment system Crossing with existing system
3.12	Underground power supply to the administrative building "BA"
3.13	Underground power supply to the secondary building "BS" from the "BI".
3.14	Underground telecommunication power supply
3.15	TI to coordinate with the CPA (Parks Canada Agency)
3.16	Radiocommunication to coordinate with the CPA
3.17 C	Construction of part of the parking lot of the administrative building "BA".
3.18	Soil preparation and earthworks
3.19	Existing underground telecommunication line to be preserved
3.20	Connection of underground power supply to the well
3.21	Connection of the power supply to the charging stations of the administrative building (BA)
3.22	Installation of the water supply line for the industrial building "BI".
3.23	Installation of conduits for the electrical supply of the industrial building "BI"
3.24	Connection of the generator power supply
3.25	Connection of power supply to water treatment system
3.26	Temporary fencing installation to limit access to existing facilities
3.27	Installation of a section of conduit for power supply to the motorized barrier
3.28	Removal of the remaining section of the water supply of the conservation building
3.29	Installation of a section of the pipes for the power supply of the petrol station
3.30	Installation of a section of conduit for power supply to the de-icing salt shelter
3.31	New closure between the BA and the BI
3.32	Demolition of a section of the sanitary sewer of the Technical Services Building
3.33	Demolition of the existing leaching field
3.34	Temporary connection of the sanitary sewer from the Engineering Services Building to the new water treatment system
3.35	Connection of the power supply to the industrial building (BI) charging stations
3.36	Construction of the industrial building "BI"
3.37	Partial removal of underground power supply from the Technical Services Building
3.38	Partial removal of the communication line from the conservation building.
3.39	Storm Sewer Installation
3.40	Sanitary sewer installation
3.41	Installation of a flagpole




2019-04-19

**TETRA TECH**


2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-606-8224

**JBCA**architectes

Project:		Project number :	
Operational Center Repair & administrative center layout		1415	
		Annex number :	
Works phasing		ANNEX 1	
		Date :	Drawing :
		2019-02-25	03/11

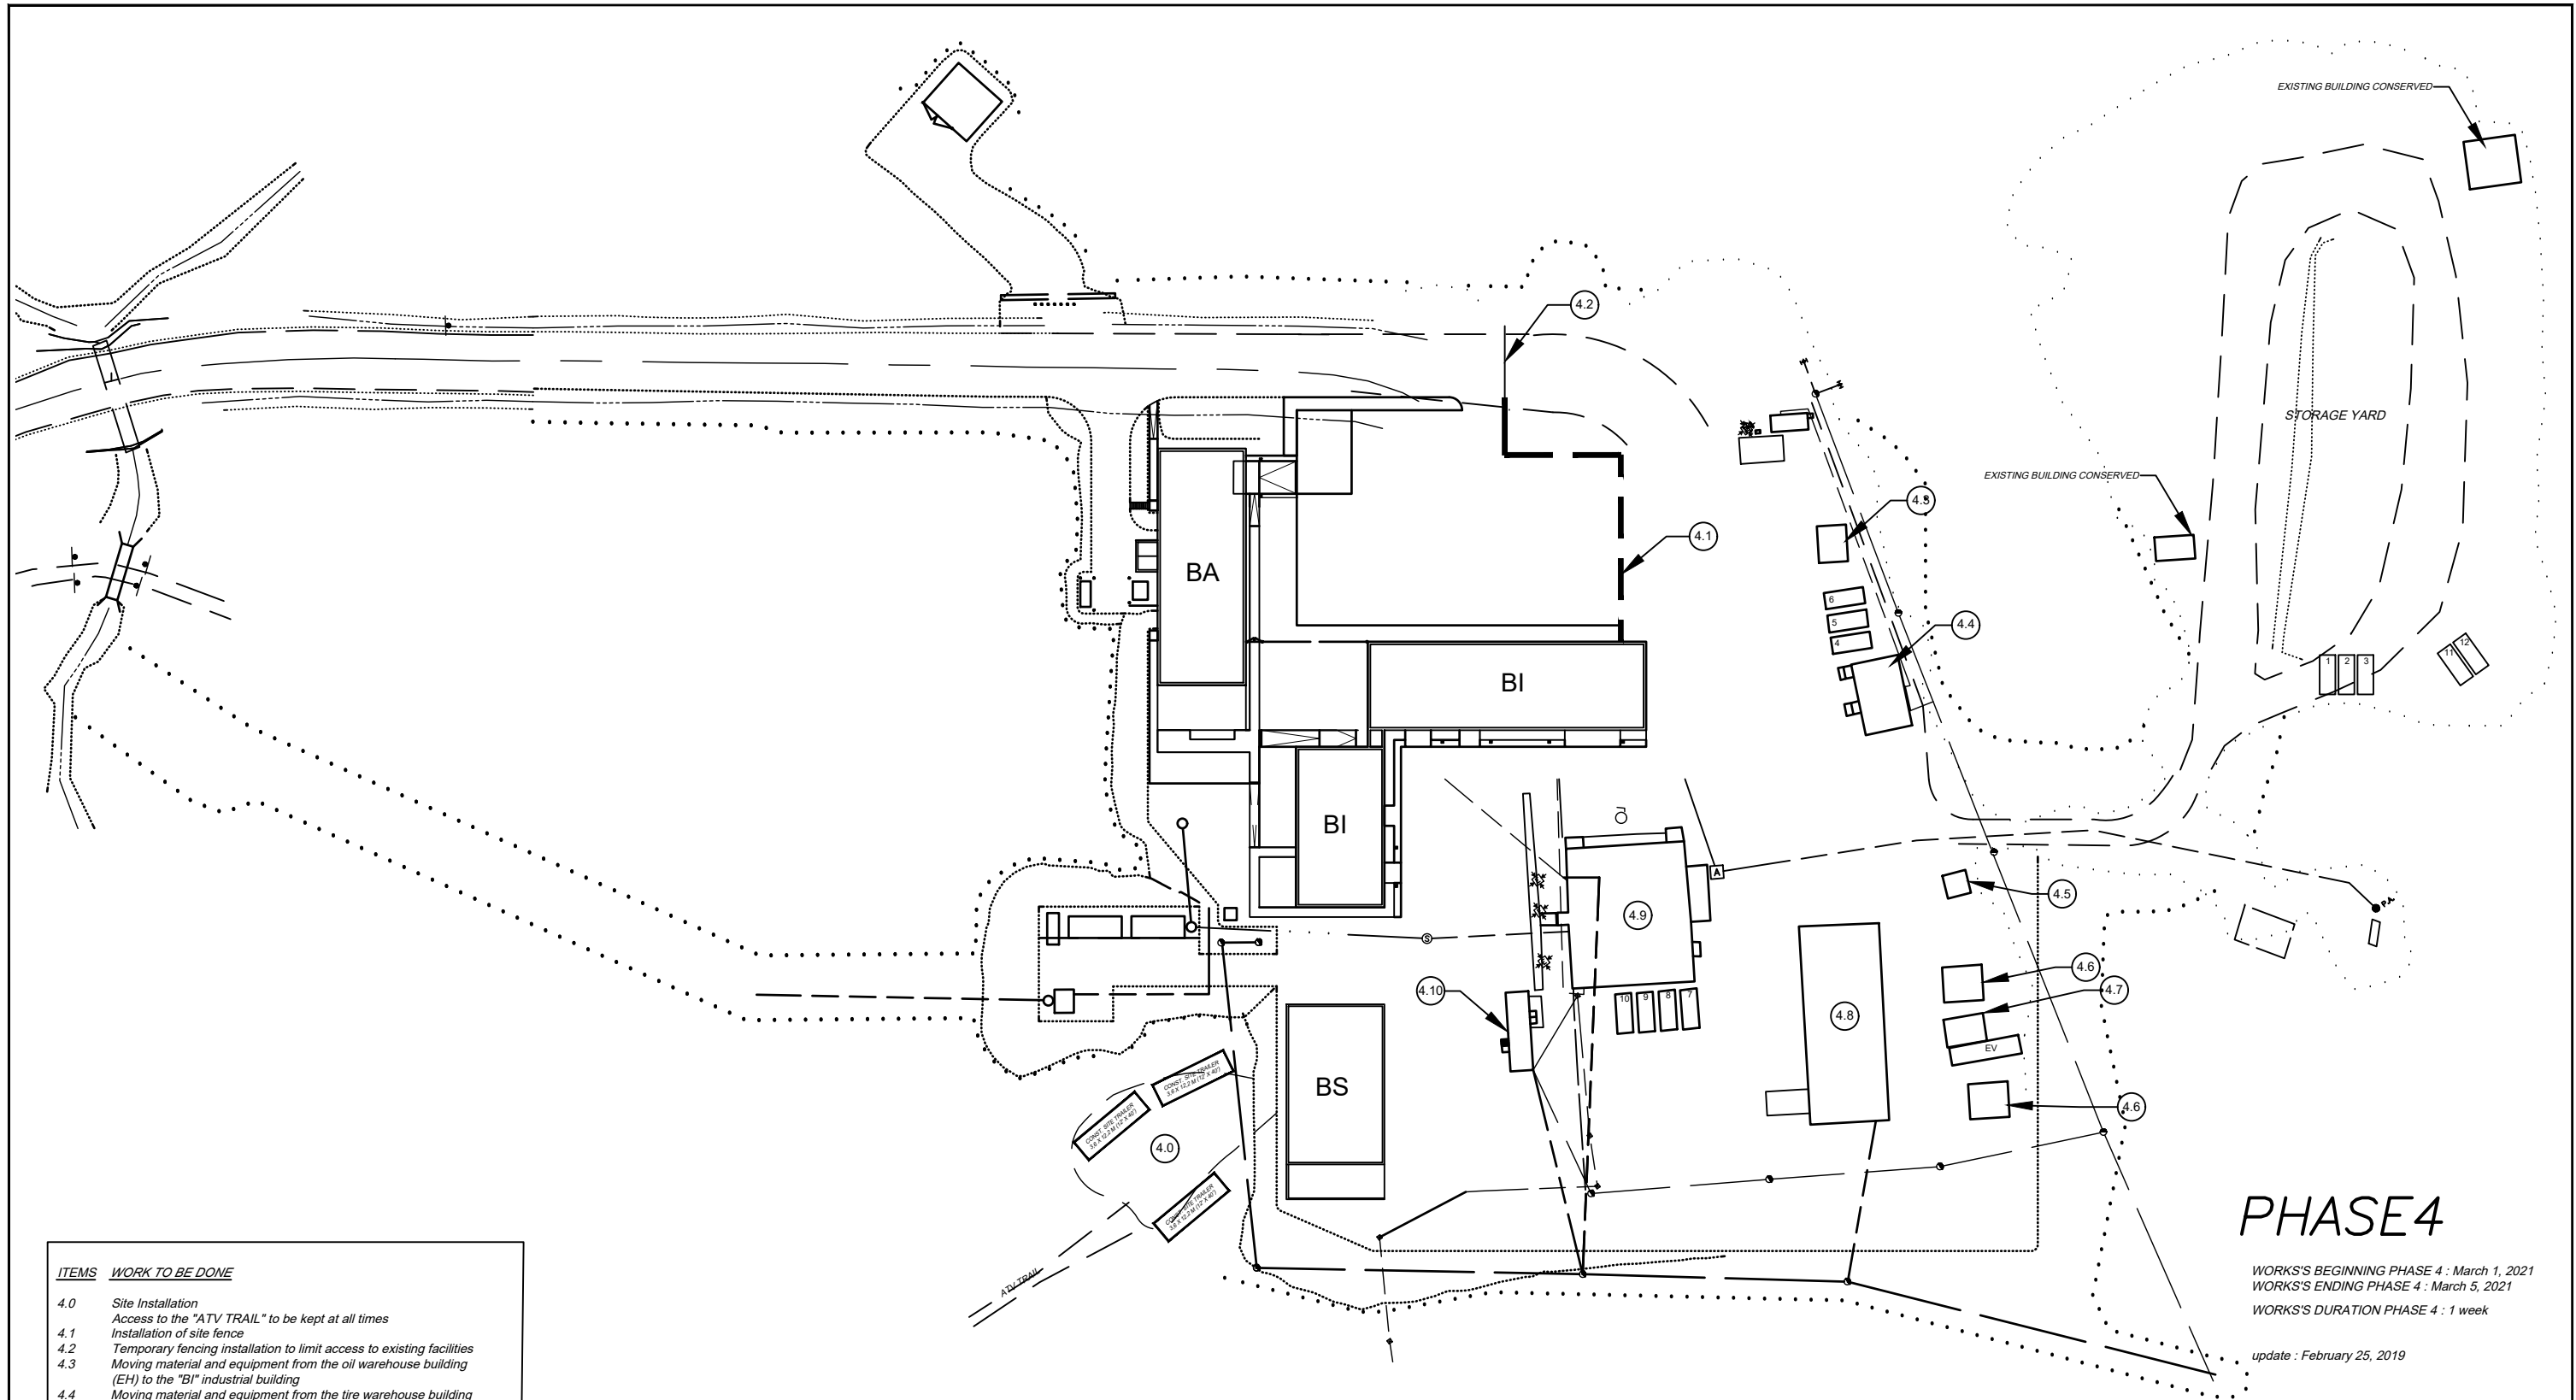

PHASE4

WORKS'S BEGINNING PHASE 4 : March 1, 2021
WORKS'S ENDING PHASE 4 : March 5, 2021
WORKS'S DURATION PHASE 4 : 1 week

update : February 25, 2019

ITEMS WORK TO BE DONE

- 4.0 Site Installation
Access to the "ATV TRAIL" to be kept at all times
- 4.1 Installation of site fence
- 4.2 Temporary fencing installation to limit access to existing facilities
- 4.3 Moving material and equipment from the oil warehouse building (EH) to the "BI" industrial building
- 4.4 Moving material and equipment from the tire warehouse building (EP) to the secondary building "BS".
- 4.5 Moving material and equipment from the Chemical Warehouse Building (CWB) to the "BI" industrial building
- 4.6 Moving material and equipment from the canvas shelters to the secondary building "BS".
- 4.7 Moving material and equipment from the warehouse building "trail building" to the industrial building "BI".
- 4.8 Moving material and equipment from the "ATCO" building to the secondary building "BS".
- 4.9 Moving material and equipment from the technical services building to the "BI" industrial building
- 4.10 Moving equipment and workstations from the trailer Projects & TSB to the administrative building "BA".

ADD- A02



2019-04-19



stgm

2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-626-8224



TETRA TECH



JBCA architectes

Project:

Operational Center Repair
& administrative center layout

Works phasing

Project number :

1415

Annex number :


ANNEX 1

Date :

2019-02-25

Drawing :

04/11

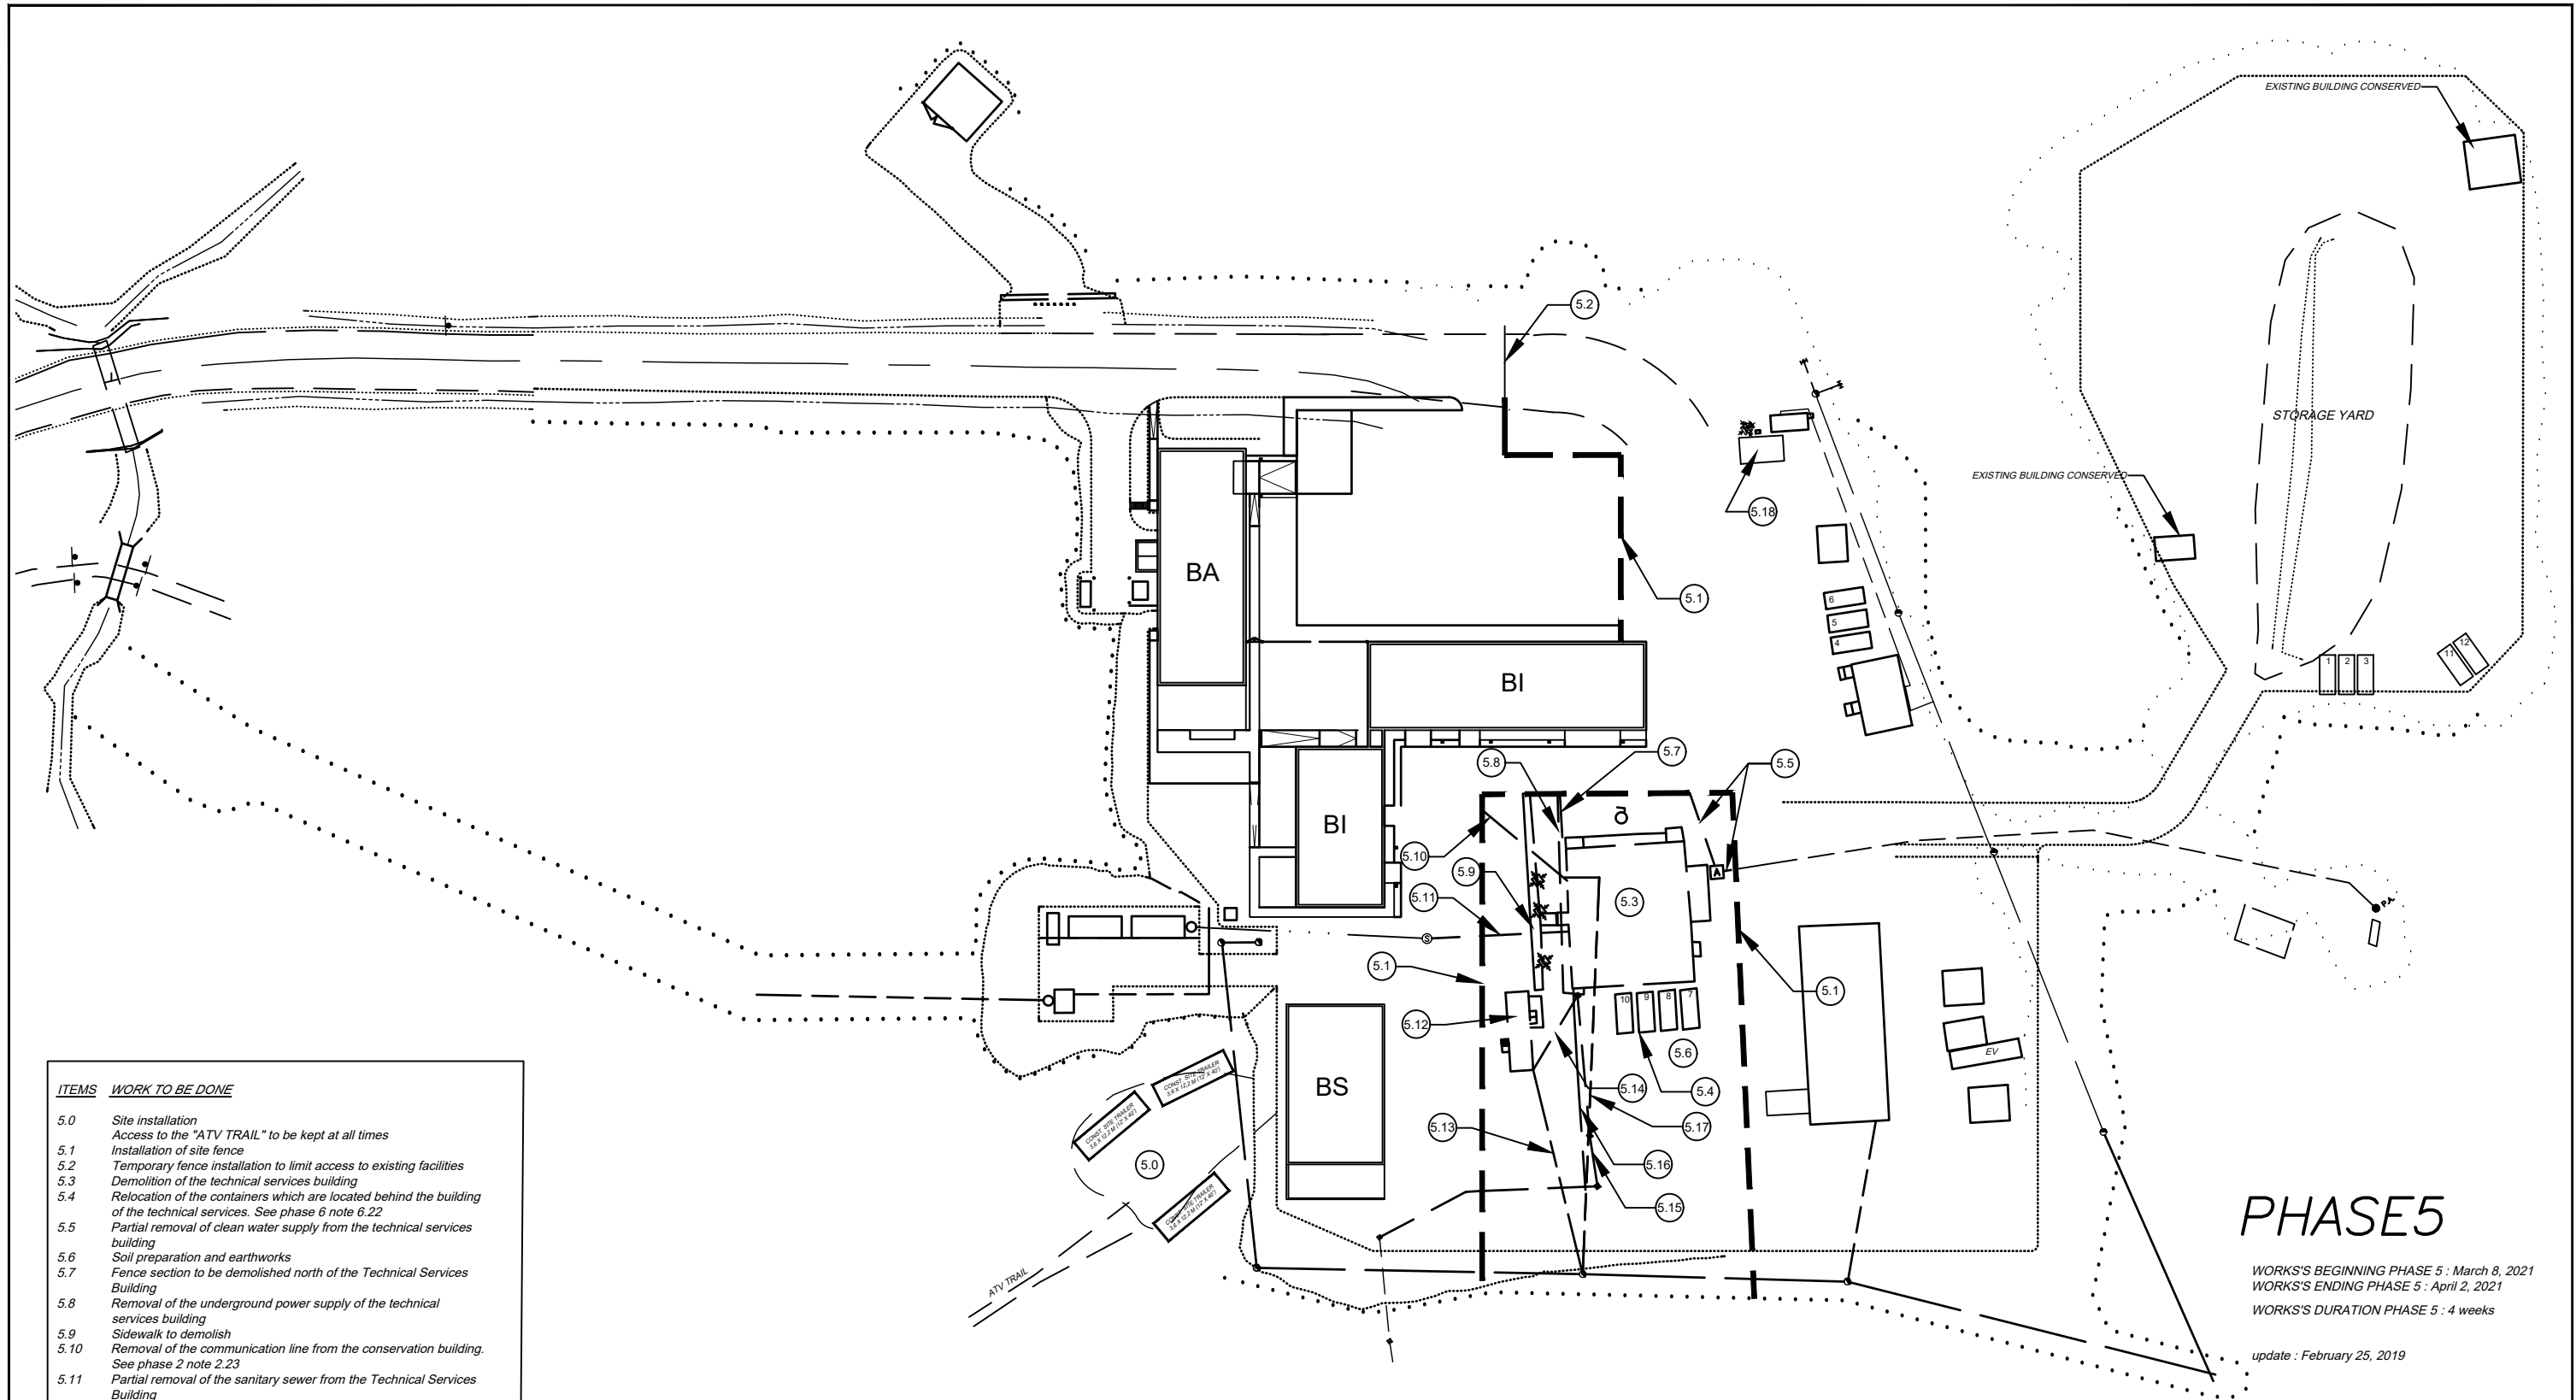

PHASE5

WORKS'S BEGINNING PHASE 5 : March 8, 2021
WORKS'S ENDING PHASE 5 : April 2, 2021
WORKS'S DURATION PHASE 5 : 4 weeks

update : February 25, 2019

ITEMS	WORK TO BE DONE
5.0	Site installation Access to the "ATV TRAIL" to be kept at all times
5.1	Installation of site fence
5.2	Temporary fence installation to limit access to existing facilities
5.3	Demolition of the technical services building
5.4	Relocation of the containers which are located behind the building of the technical services. See phase 6 note 6.22
5.5	Partial removal of clean water supply from the technical services building
5.6	Soil preparation and earthworks
5.7	Fence section to be demolished north of the Technical Services Building
5.8	Removal of the underground power supply of the technical services building
5.9	Sidewalk to demolish
5.10	Removal of the communication line from the conservation building. See phase 2 note 2.23
5.11	Partial removal of the sanitary sewer from the Technical Services Building
5.12	Move the "Project" trailer into the storage yard. See phase 6 note 6.21
5.13	Removal of the overhead power supply to the trailer "Project".
5.14	Removal of the overhead telecommunication line between the "Project" trailer and the Technical Services Building
5.15	Removal of the underground telecommunication line from the Technical Services Building
5.16	Fence to be demolished in the south of the technical services building
5.17	Removal of the temporary overhead power supply from the Technical Services Building
5.18	Wi-Fi link from the gas station to be moved from the technical services building to the new industrial building




2019-04-19



stgm
2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-626-8224



Project:		Project number :	
Operational Center Repair & administrative center layout		1415	
		Annex number :	
		ANNEX 1	
Works phasing		Date :	Drawing :
		2019-02-25	05/11

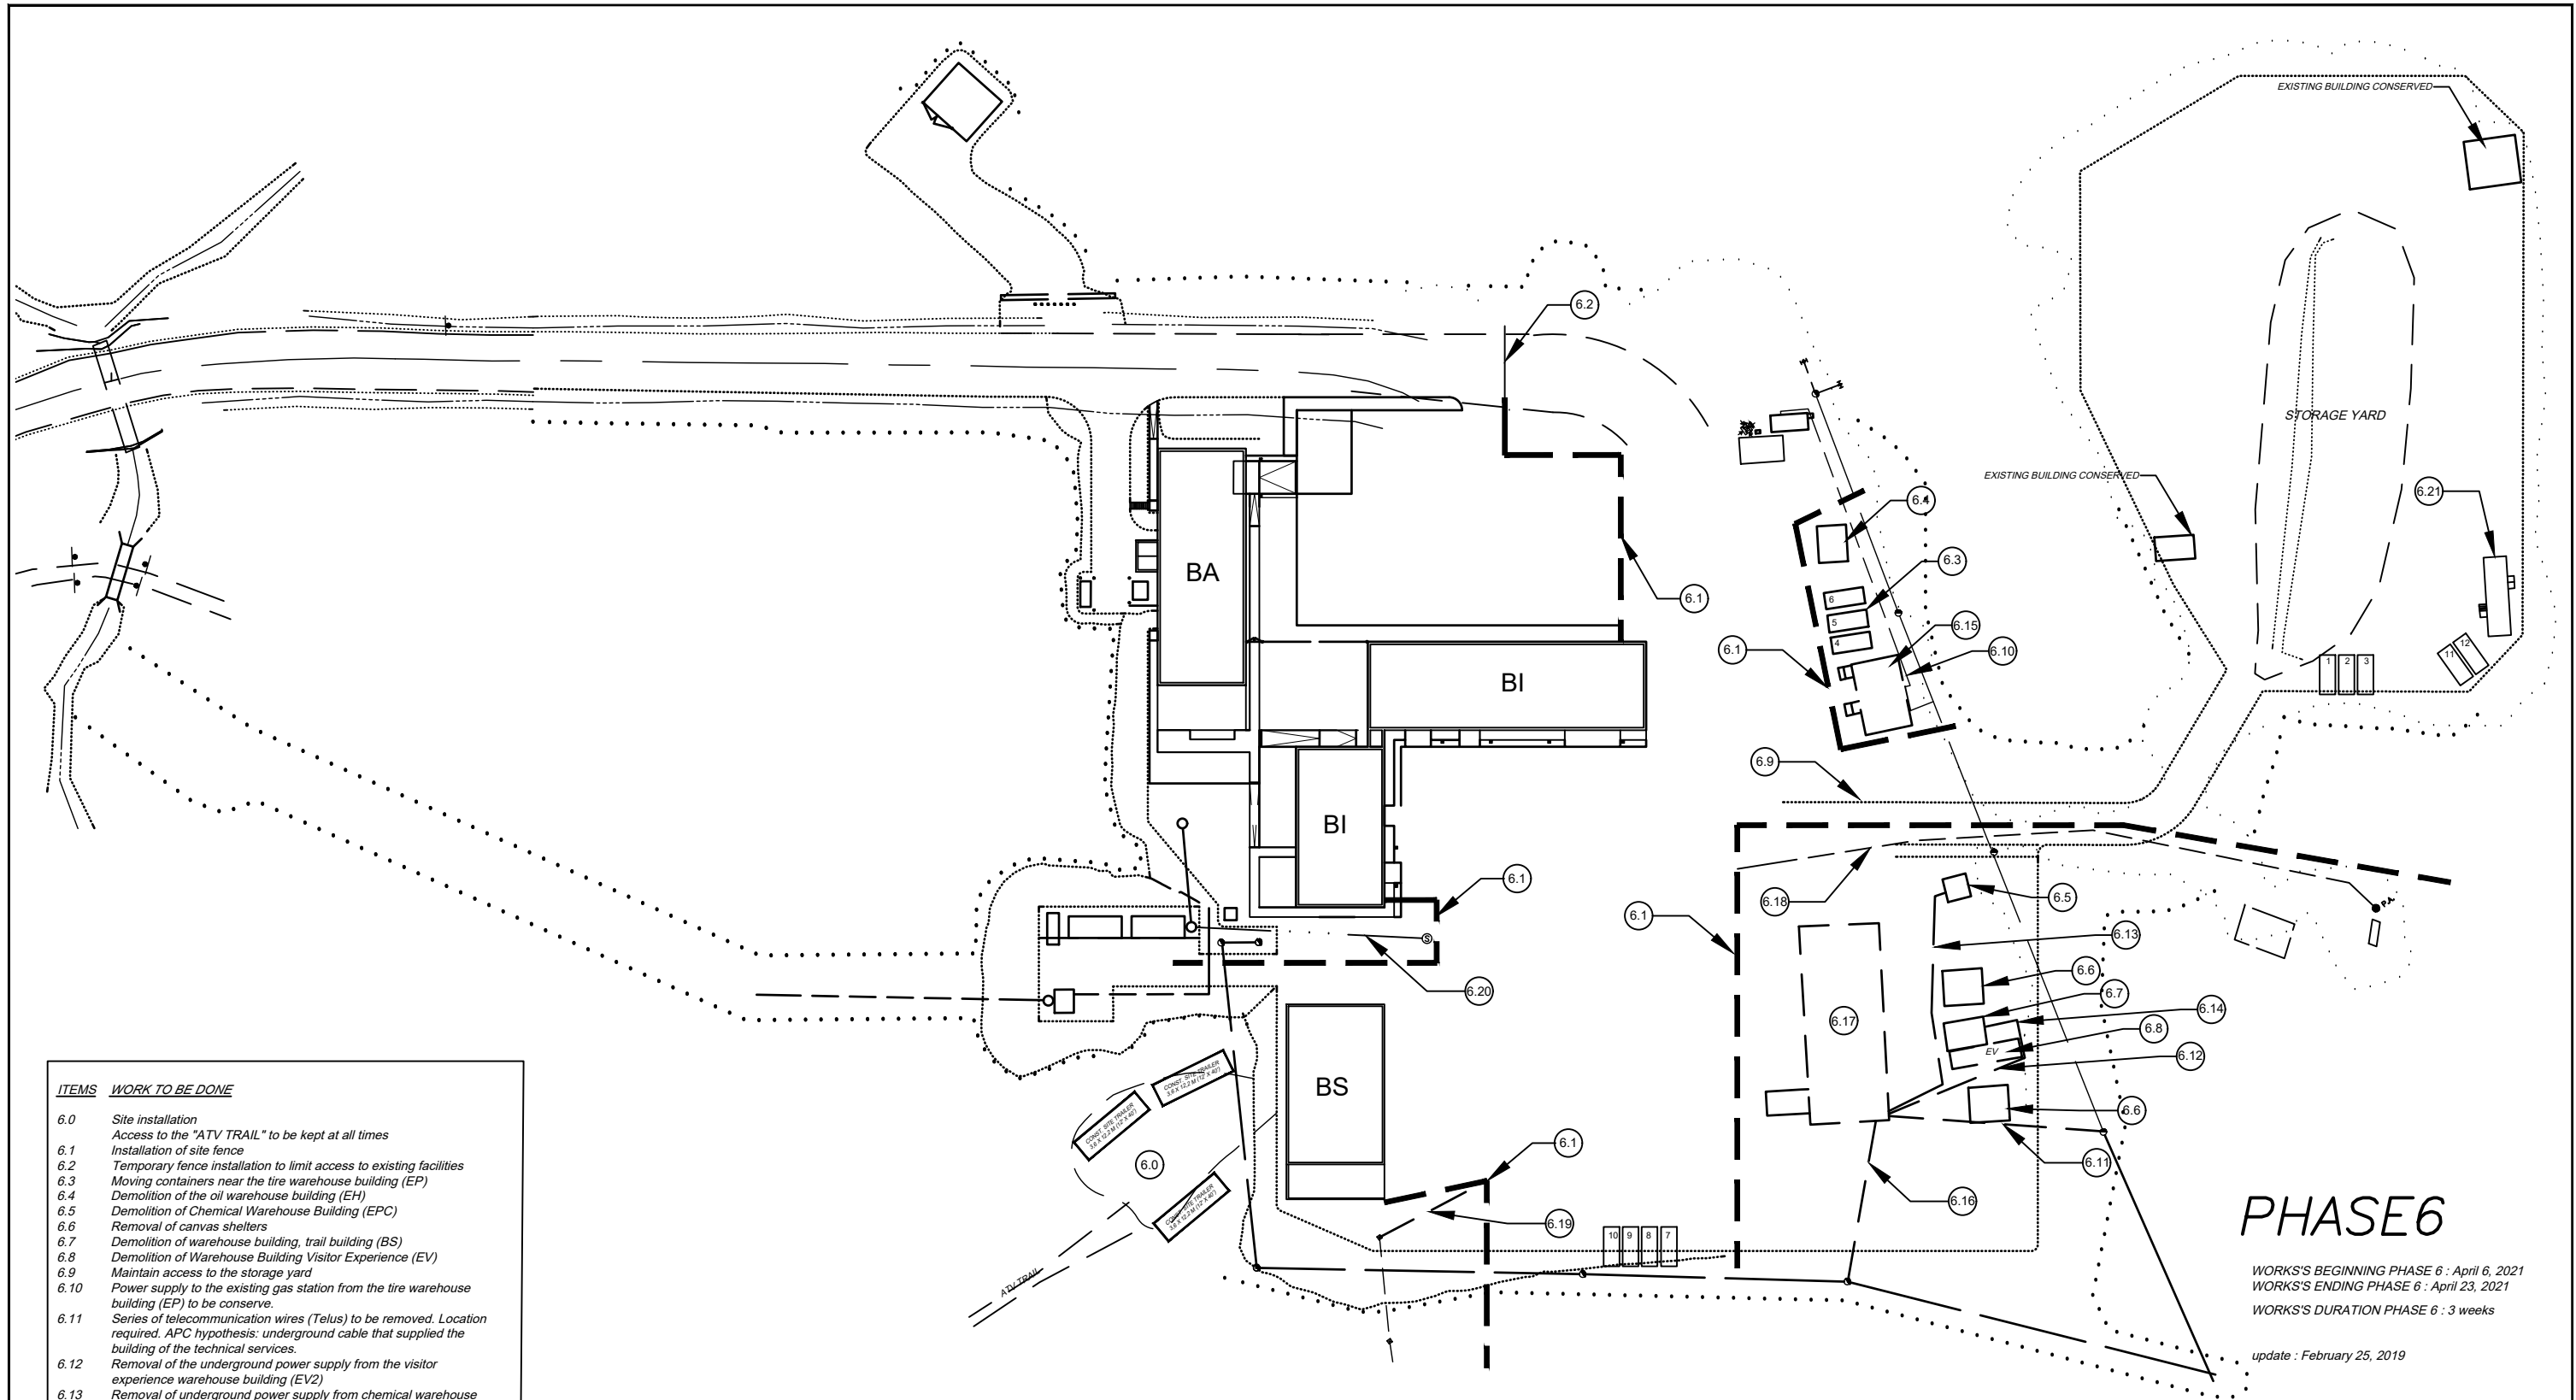

PHASE6

WORKS'S BEGINNING PHASE 6 : April 6, 2021
WORKS'S ENDING PHASE 6 : April 23, 2021
WORKS'S DURATION PHASE 6 : 3 weeks

update : February 25, 2019

ITEMS WORK TO BE DONE

- 6.0 Site installation
Access to the "ATV TRAIL" to be kept at all times
- 6.1 Installation of site fence
- 6.2 Temporary fence installation to limit access to existing facilities
- 6.3 Moving containers near the tire warehouse building (EP)
- 6.4 Demolition of the oil warehouse building (EH)
- 6.5 Demolition of Chemical Warehouse Building (EPC)
- 6.6 Removal of canvas shelters
- 6.7 Demolition of warehouse building, trail building (BS)
- 6.8 Demolition of Warehouse Building Visitor Experience (EV)
- 6.9 Maintain access to the storage yard
- 6.10 Power supply to the existing gas station from the tire warehouse building (EP) to be conserve.
- 6.11 Series of telecommunication wires (Telus) to be removed. Location required. APC hypothesis: underground cable that supplied the building of the technical services.
- 6.12 Removal of the underground power supply from the visitor experience warehouse building (EV2)
- 6.13 Removal of underground power supply from chemical warehouse building (EPC)
- 6.14 Removal of underground power supply between visitor experience warehouse building (EV2) and warehouse building trail (BS)
- 6.15 Demolition of the Tire Warehouse Building (EP)
- 6.16 Removing the power supply of the ATCO building
- 6.17 Demolition of the ATCO building
- 6.18 Removal of clean water supply from the technical services building to the well
- 6.19 Removal of a section of the underground telecommunication line
- 6.20 Removal of temporary connection of the sanitary sewer from the technical services building to the new water treatment system
- 6.21 New location of the trailer "Projects"
- 6.22 Relocated containers. See phase 5 note 5.4



2019-04-19



stgm

2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-626-8224



TETRA TECH



JBCA architectes

Project:

Operational Center Repair
& administrative center layout

Works phasing

Project number :

1415

Annex number :


ANNEX 1

Date :

2019-02-25

Drawing :

06/11

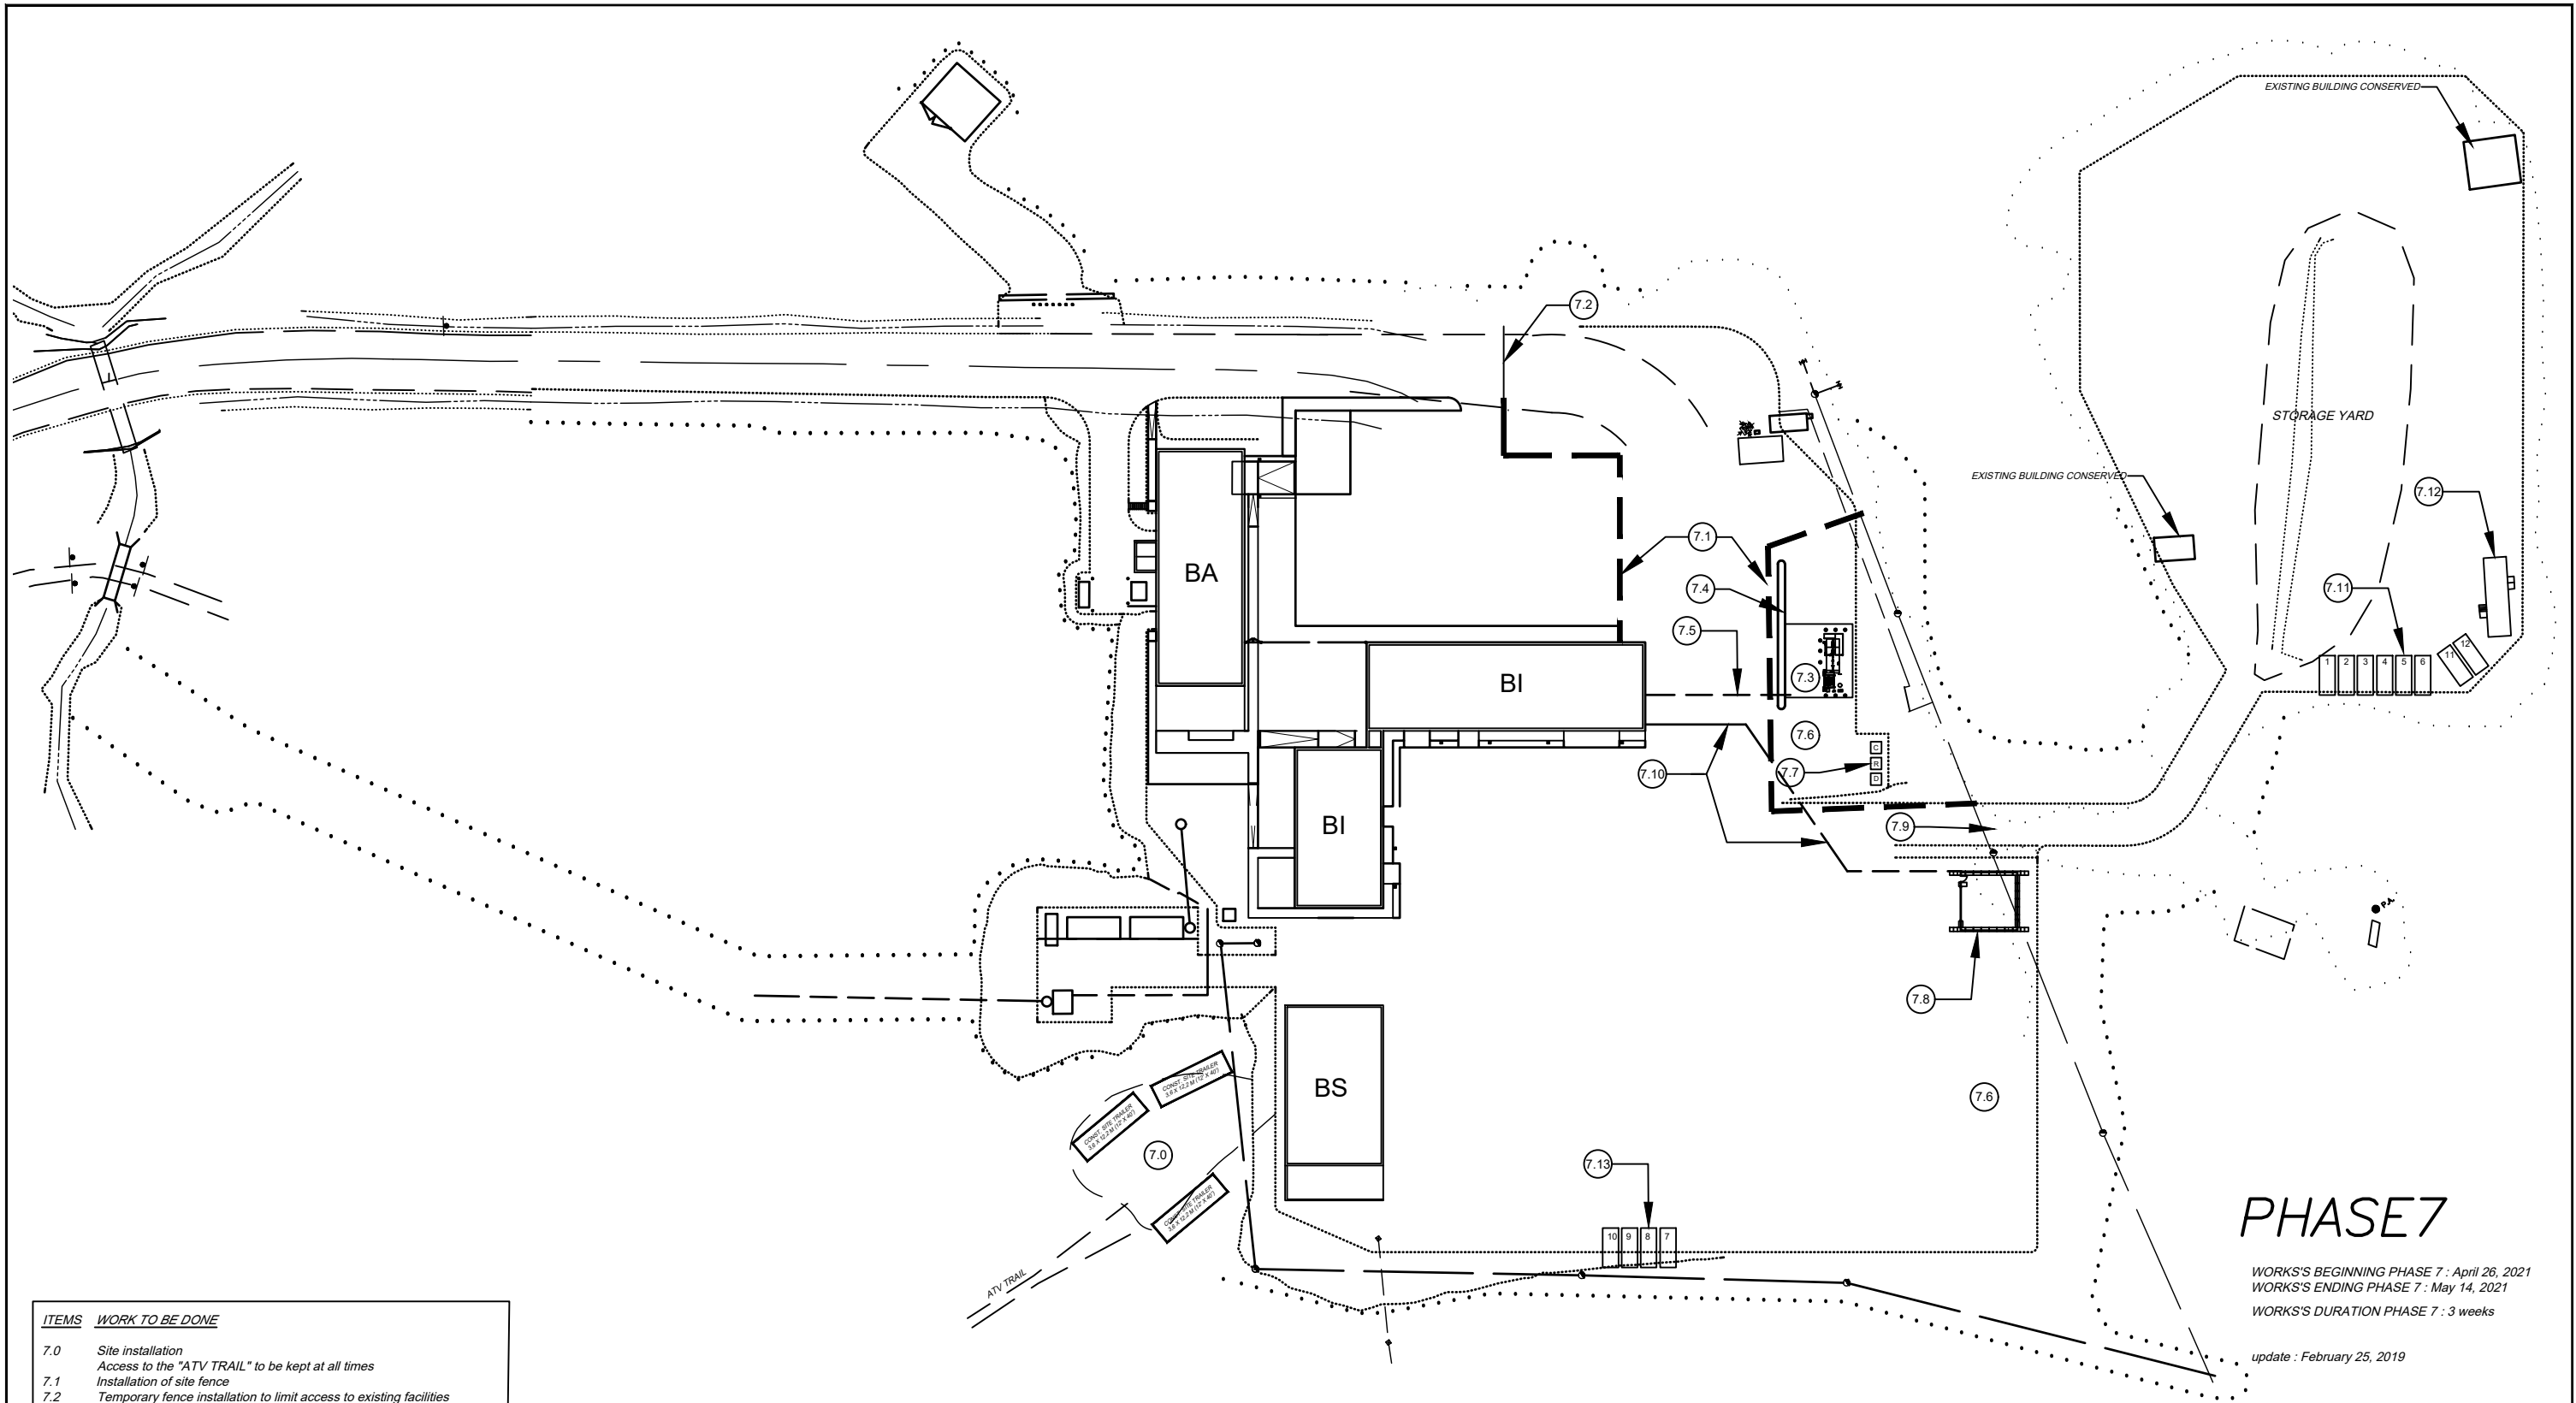

PHASE 7

WORKS'S BEGINNING PHASE 7 : April 26, 2021
WORKS'S ENDING PHASE 7 : May 14, 2021
WORKS'S DURATION PHASE 7 : 3 weeks

update : February 25, 2019

ITEMS	WORK TO BE DONE
7.0	Site installation Access to the "ATV TRAIL" to be kept at all times
7.1	Installation of site fence
7.2	Temporary fence installation to limit access to existing facilities
7.3	Construction of the gas station
7.4	Building the island
7.5	Power supply connection of the gas station. Work to be done in 2 sections to allow vehicles to circulate at all time.
7.6	Soil preparation and earthworks
7.7	Container installation (residual materials)
7.8	Construction of the de-icing salt shelter
7.9	Maintain access to the storage yard
7.10	Power supply connection of the de-icing salt shelter. Work to be done in 2 sections to allow vehicles to circulate at all times
7.11	Relocated containers
7.12	Relocated the project caravan
7.13	Relocated containers. See phase 8 note 8.8




2019-04-19

**TETRA TECH**

**JBCA**architectes

**stgm**
2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-626-8224

Project: Operational Center Repair & administrative center layout		Project number : 1415	
Works phasing		Annex number : ANNEX 1	
		Date : 2019-02-25	Drawing : 07/11

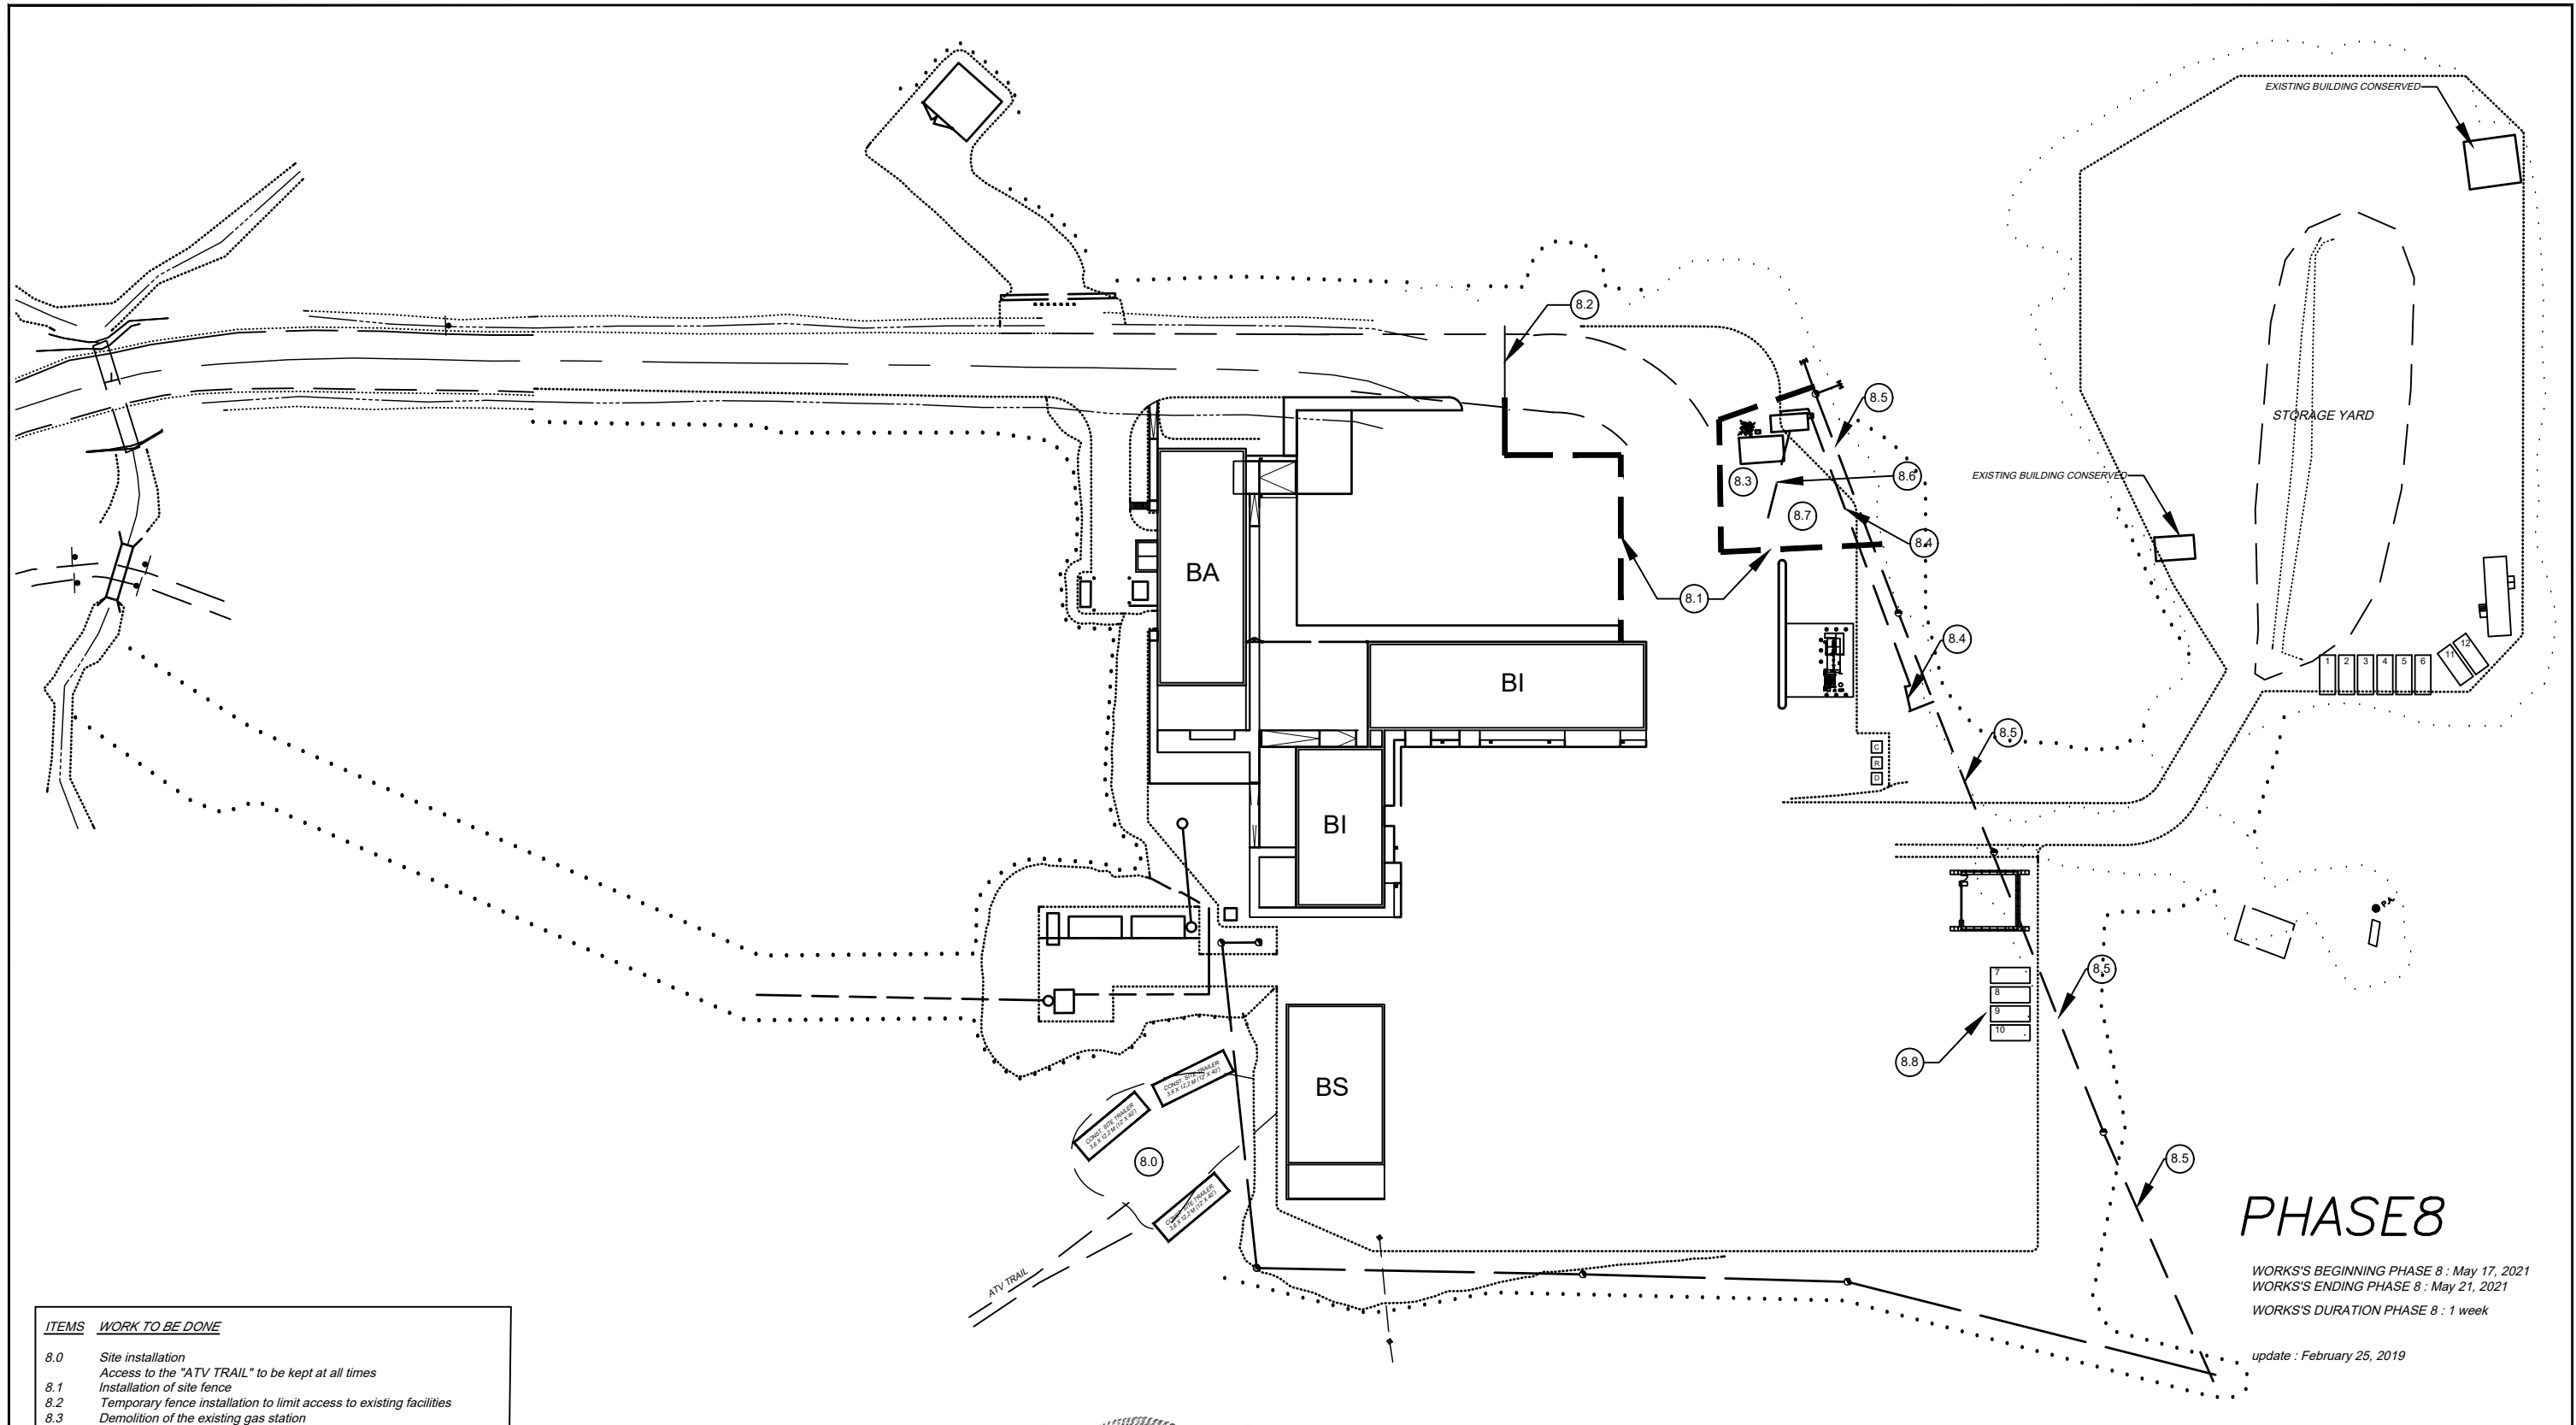

PHASE8

WORKS'S BEGINNING PHASE 8 : May 17, 2021
WORKS'S ENDING PHASE 8 : May 21, 2021
WORKS'S DURATION PHASE 8 : 1 week

update : February 25, 2019

ITEMS WORK TO BE DONE

- 8.0 Site installation
Access to the "ATV TRAIL" to be kept at all times
- 8.1 Installation of site fence
- 8.2 Temporary fence installation to limit access to existing facilities
- 8.3 Demolition of the existing gas station
- 8.4 Removal of the power supply from the existing gas station
- 8.5 Removal of the overhead power line
- 8.6 Removal of an old underground wire that connected the gas station to a workstation in the technical services building
- 8.7 Soil preparation and earthworks
- 8.8 Relocated containers

IMPORTANT NOTE :

The delivery and installation of furniture (by PCA) of the Administrative Building (BA) should be done at the latest during the work of phase 8.



2019-04-19



stgm

2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-606-8224



TETRA TECH



architectes

Project:

Operational Center Repair
& administrative center layout

Works phasing

Project number :

1415

Annex number :


ANNEX 1

Date :

2019-02-25

Drawing :

08/11

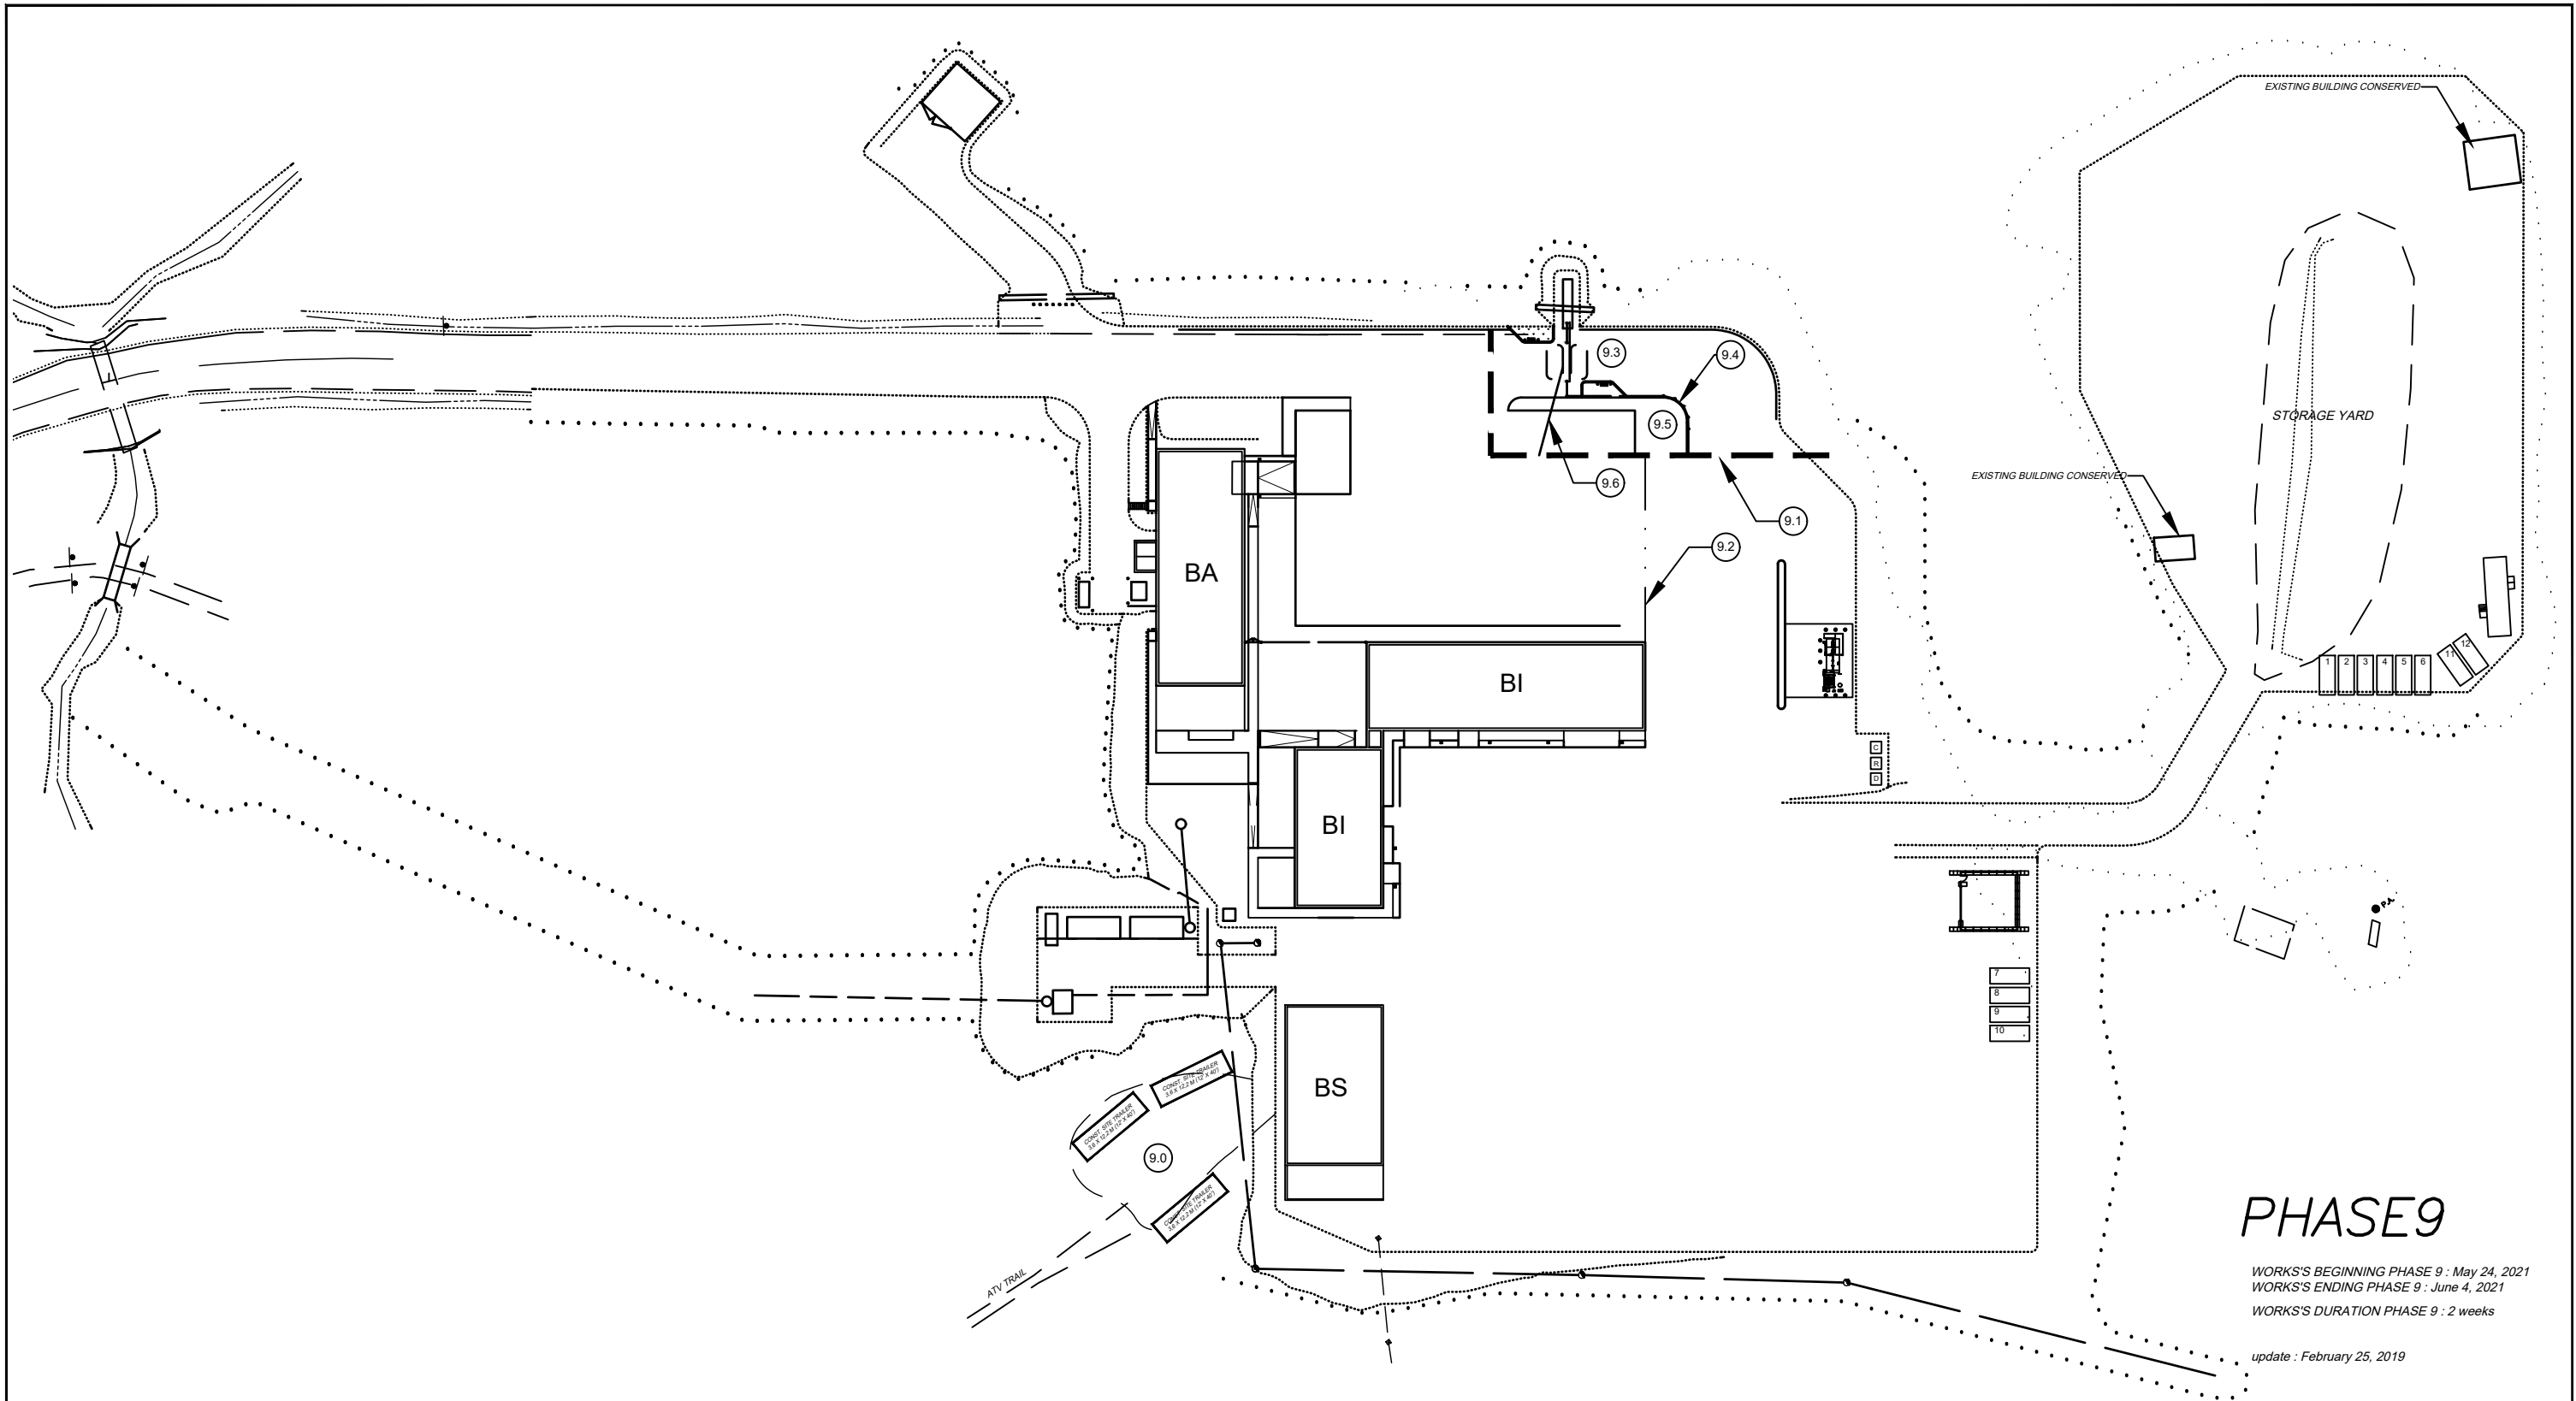

PHASE9

WORKS'S BEGINNING PHASE 9 : May 24, 2021
WORKS'S ENDING PHASE 9 : June 4, 2021
WORKS'S DURATION PHASE 9 : 2 weeks

update : February 25, 2019

ITEMS WORK TO BE DONE

- 9.0 Site installation
Access to the "ATV TRAIL" to be kept at all times
- 9.1 Installation of site fence
- 9.2 Temporary fence installation to limit access to existing facilities
- 9.3 Installation of the motorized barrier
- 9.4 Installation of a fence section
- 9.5 Soil preparation and earthworks
- 9.6 Connection for power supply of the motorized barrier. See phase 3 note 3.27



2019-04-19



stgm

2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-626-8224



TETRA TECH



JBCA architectes

Project:

Operational Center Repair
& administrative center layout

Works phasing

Project number :

1415

Annex number :


ANNEX 1

Date :

2019-02-25

Drawing :

09/11

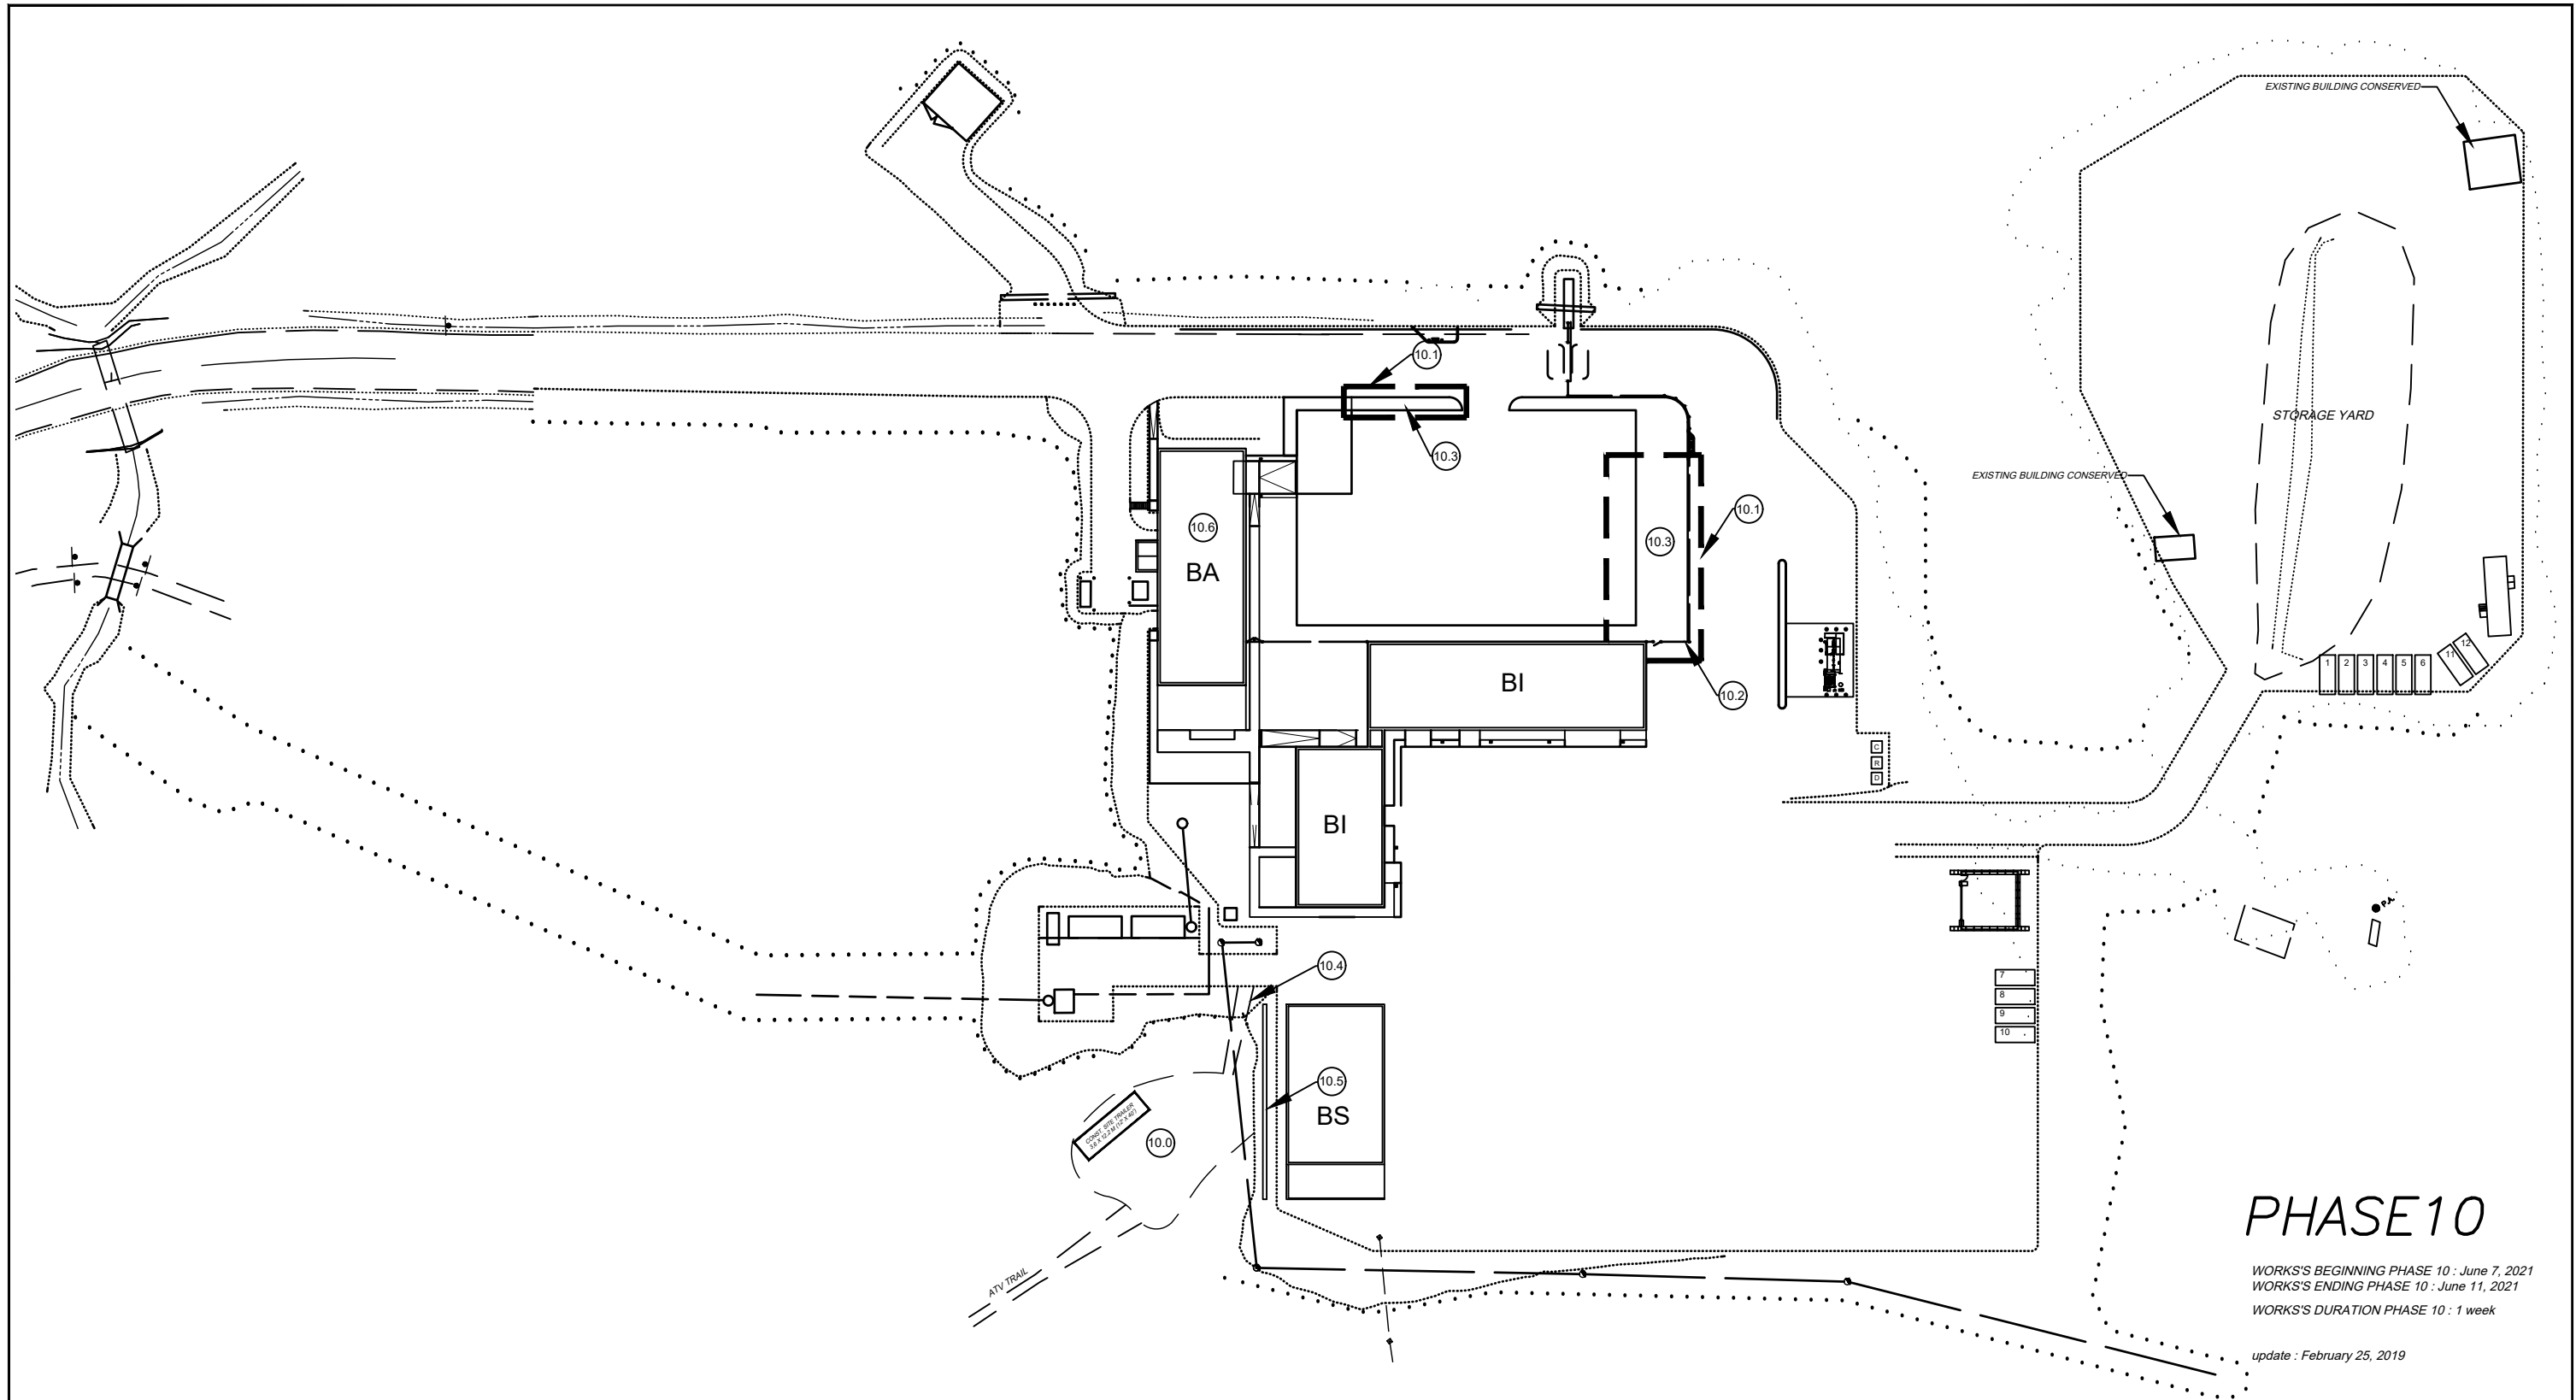

PHASE 10

WORKS'S BEGINNING PHASE 10 : June 7, 2021
WORKS'S ENDING PHASE 10 : June 11, 2021
WORKS'S DURATION PHASE 10 : 1 week

update : February 25, 2019

ITEMS	WORK TO BE DONE
10.0	Site installation Access to the "ATV TRAIL" to be kept at all times
10.1	Installation of site fence
10.2	Installation of a fence section
10.3	Soil preparation and earthworks
10.4	ATV trail access
10.5	Hose support installation
10.6	Relocation of temporary layouts and Gaspé office to the administrative building and the industrial building

ADD- A02



2019-04-19



stgm

2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-636-8224



Project:
Operational Center Repair
& administrative center layout

Works phasing

Project number :

1415

Annex number :


ANNEX 1

Date :

Drawing :

2019-02-25

10/11

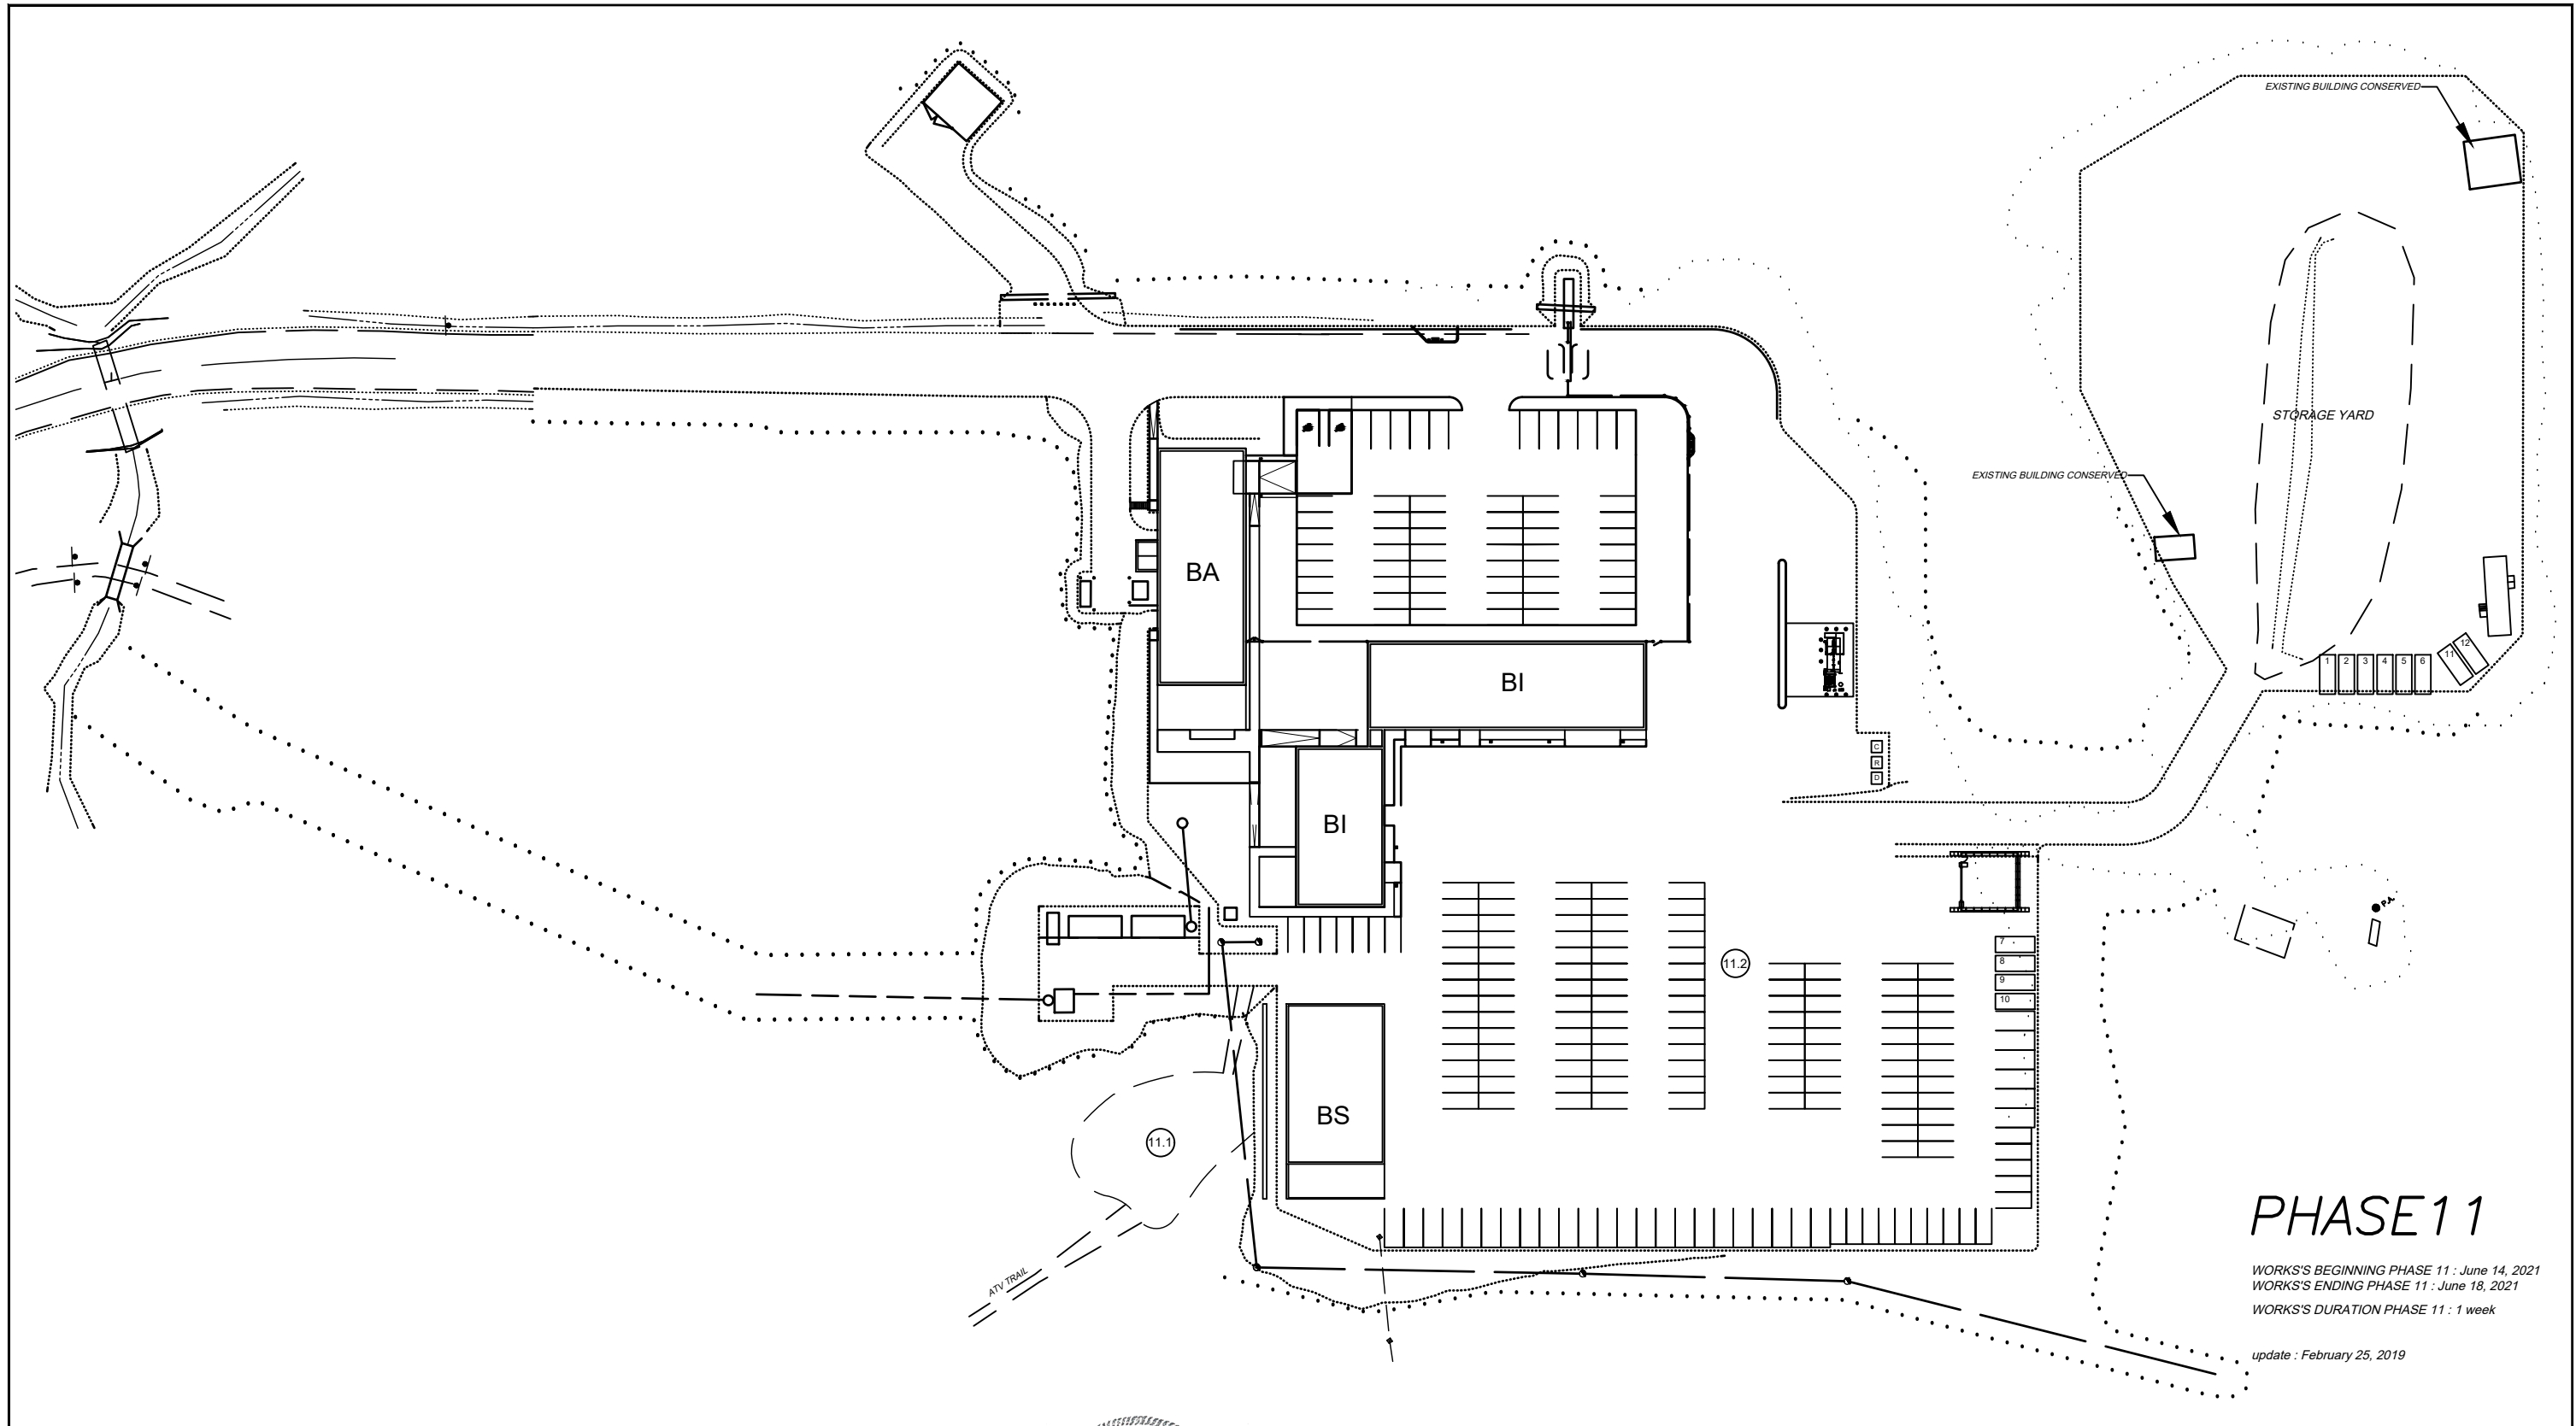

PHASE 11

WORKS'S BEGINNING PHASE 11 : June 14, 2021
WORKS'S ENDING PHASE 11 : June 18, 2021
WORKS'S DURATION PHASE 11 : 1 week

update : February 25, 2019

ITEMS	WORK TO BE DONE
11.1	Contractor's demobilization
11.2	Final cleaning



2019-04-19



stgm

2980, boul. Sainte-Anne, Québec (QC), Canada, G1E 3J3
418-606-8224



Project:		Project number :	
Operational Center Repair & administrative center layout		1415	
		Annex number :	
		ANNEX 1	
Works phasing		Date :	Drawing :
		2019-02-25	11/11
