


prime consultant:

ARCHITECTURE 49

sub consultant:



APPROX. NORTH

PHASING OBJECTIVES:

PHASE 7 (RENOVATE DEPARTURE VESTIBULE AND ADJACENT CONCOURSE):

SCHEDULE: DURATION 2 WEEKS

1. TEMPORARY SHUT DOWN OF EXISTING DEPARTURES VESTIBULE.
2. PASSENGER DEPARTURE: PASSENGERS DEPARTS THROUGH NEW ARRIVALS VESTIBULE 136, PROCEED TO NEW TICKETING COUNTERS, DROP BAGGAGE AT NEW CATSA HBS, PROCEED TO CATSA PBS.
3. PASSENGER ARRIVALS: PASSENGERS ARRIVE THROUGH NEW VESTIBULE 123, CLAIM BAGGAGE AT NEW BAGGAGE CLAIM 121, PROCEED TO NEW ARRIVALS VESTIBULE 136.
4. CONSTRUCTION MOBILIZATION AND ASBESTOS ABATEMENT.
5. RENOVATE/CONSTRUCT NEW DEPARTURES VESTIBULE 100, RENOVATE EXISTING STAIRWELL 103, CONSTRUCT NEW AIRSIDE VESTIBULE 120, RENOVATE PBS FLOORING DURING NIGHTSHIFT WORK.
6. SCREENED PASSENGERS TO DEPART FROM VEST 122
7. TEMPORARILY RELOCATE PA ACCESS FROM VEST 120 TO VEST 122
8. RENOVATE CONCOURSE AREA LOCATED WITHIN PHASE 7 (INCL ARCHITECTURAL, MECHANICAL, ELECTRICAL AND FIRE SUPPRESSION), CONTRACTOR TO ENSURE ACCESS TO CATSA PBS MAINTAINED AT ALL TIMES.
9. MOBILIZE NEW DEPARTURES VESTIBULE 100.

PHASE 8 (RENOVATE LEVEL 2 OFFICES, LEVEL 1 AIRSIDE VEST. 122# AND SURROUNDING CONCOURSE):

SCHEDULE: DURATION 8 WEEKS

10. SWING FOG TO FSS EQUIPMENT ROOM #221 C/W VOICE RECORDER SYSTEM.
11. SWING JIMNANCY TO ROOM 139.
12. SWING JILL TO ROOM # 134
13. SWING ANGELA TO ROOM # 128
14. SECURE CONSTRUCTION ZONE AND ASBESTOS ABATEMENT. FULL ABATEMENT FOR FSS ROOM REQUIRED. ALL RENOVATION WORK IN FSS ROOM TO BE DONE DURING NIGHTSHIFT
15. FSS KITCHEN # 206 AND OFFICE # 204 FLOORING WORK OVERNIGHT, BATHROOM U/S.
16. RENOVATE LEVEL 2 OFFICE AREA INCLUDING NEW MECHANICAL, ELECTRICAL AND FIRE SUPPRESSION UPGRADES.
17. RENOVATE FLIGHT SERVICES STATION. FSS TO REMAIN OCCUPIED AND OPERATIONAL AT THIS TIME. 24 OPERATION.
18. RENOVATE LEVEL 2 OFFICE AREA INCLUDING NEW MECHANICAL, ELECTRICAL AND FIRE SUPPRESSION UPGRADES.
19. RENOVATE / CONSTRUCT NEW VESTIBULE 122, AND RENOVATE PART OF CONCOURSE AREA (INCL ARCHITECTURAL, MECHANICAL, ELECTRICAL AND FIRE SUPPRESSION).
20. RETURN TCC STAFF TO LEVEL 2
21. AT END OF THIS PHASE: TC, NAVCAN SPACES FULLY RENOVATED EXCEPT EQUIPMENT ROOM #221/WORKSHOP ROOM #219/MEACH ROOM #223.


PHASE 9 (SOUTH END OFFICES FIRST FLOOR AND PART OF CONCOURSE):

SCHEDULE: DURATION 6 WEEKS

22. SOC TO MOVE TO NEW TICKETING 112
23. CATSA TO MOVE TO BOARDROOM
24. AIR CONSUL TO MOVE TO 2ND FLOOR SWING SPACE ROOM #221
25. NEW TENANT, AVJET TO TEMPORARY WORKSTATION IN CARGO ROOM # 154
26. AT END OF THIS PHASE: ALL 1st FLOOR OFFICES AND NEW SOC FULLY OPERATIONAL NSD PARTIAL CONCOURSE IS RENOVATED


PHASE 7, 8, 9 MECHANICAL HVAC:

- EXISTING AHU-1 (LOCATED MECHANICAL RM 88) SERVING LEVEL 1 BACK OF HOUSE, RESTAURANT AND ALL LEVEL 2 TO REMAIN OPERATIONAL.
- EXISTING AHU-2 (LOCATED MECHANICAL RM 88) SERVING LEVEL 1 CONCOURSE, OFFICES AND ECC TO REMAIN OPERATIONAL.
- NEW AHU-1 (LOCATED NEW MECHANICAL RM 126) TO CONTINUE TO PROVIDE HVAC AS EXISTING DUCTWORK REMOVED AND NEW INSTALLED THROUGHOUT SUBSEQUENT PHASES.
- NEW AHU-2 (LOCATED NEW MECHANICAL RM 126) OPERATIONAL SERVING SECURE DEPARTURE AND BAGGAGE HANDLING AREAS.
- NEW PHASE 2 BACK OF HOUSE OFFICES WITHOUT HVAC UNTIL PHASE 4 COMPLETION.
- NEW PHASE 3 BACK OF HOUSE OFFICES WITHOUT HVAC UNTIL PHASE 4 COMPLETION.

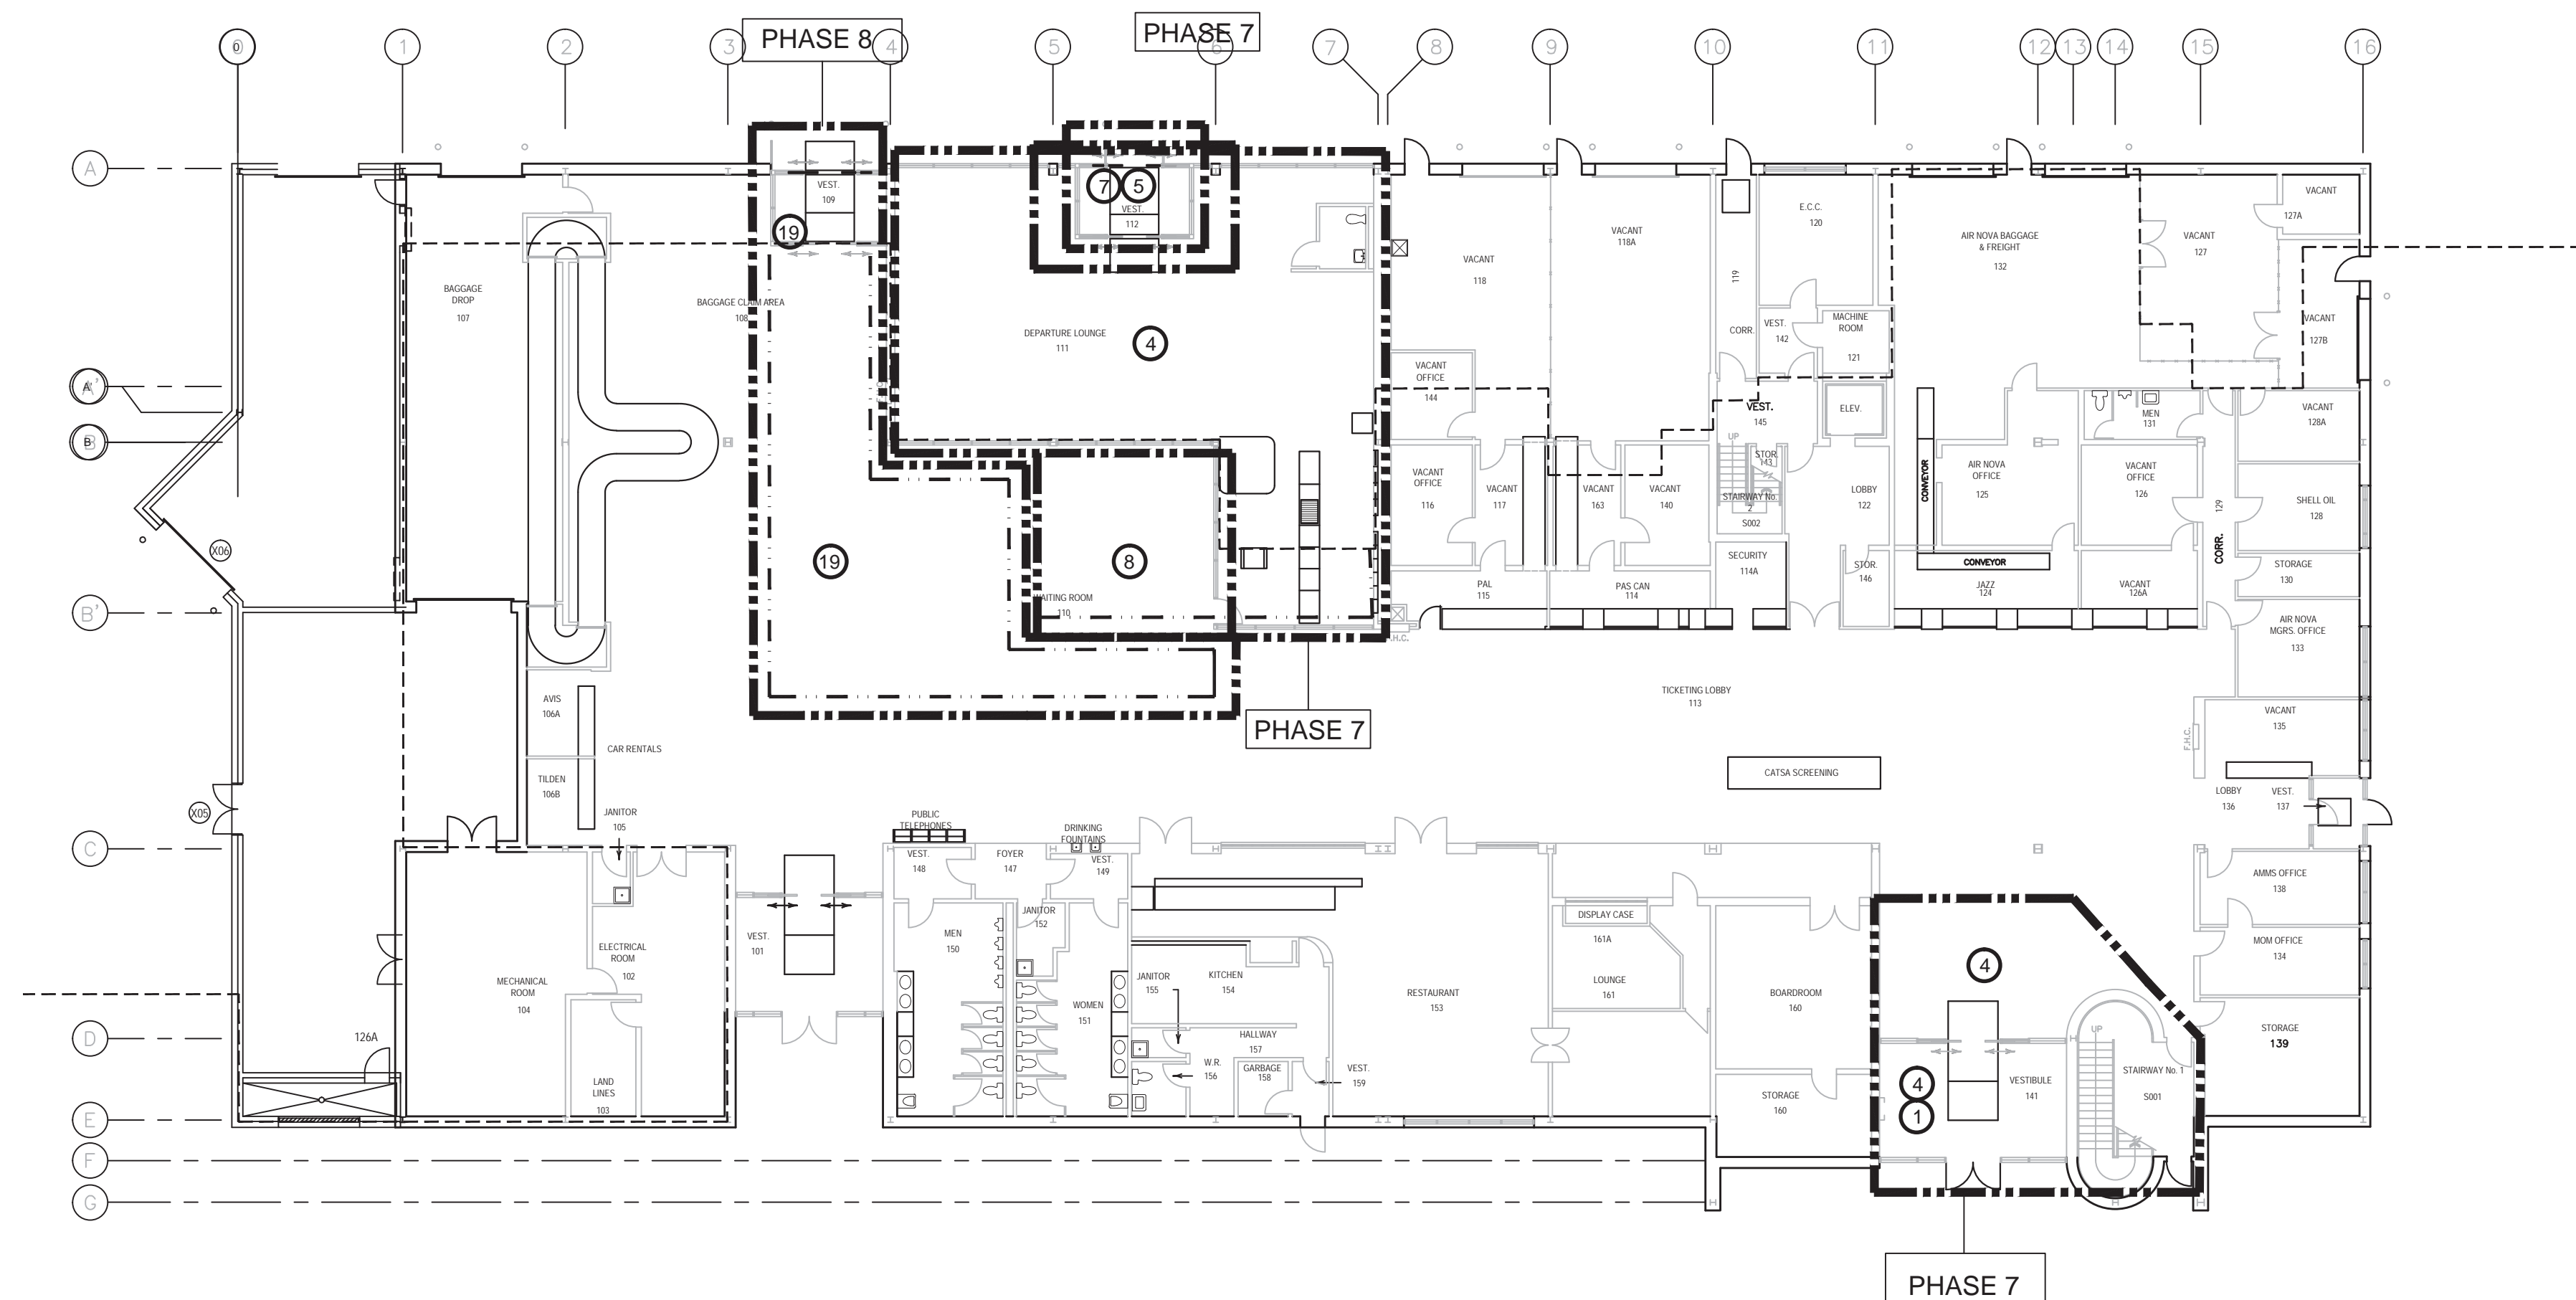


FLOOR PLAN – LEVEL 1 EXISTING, PHASE 7, 8, 9

1
A-106 | A-106

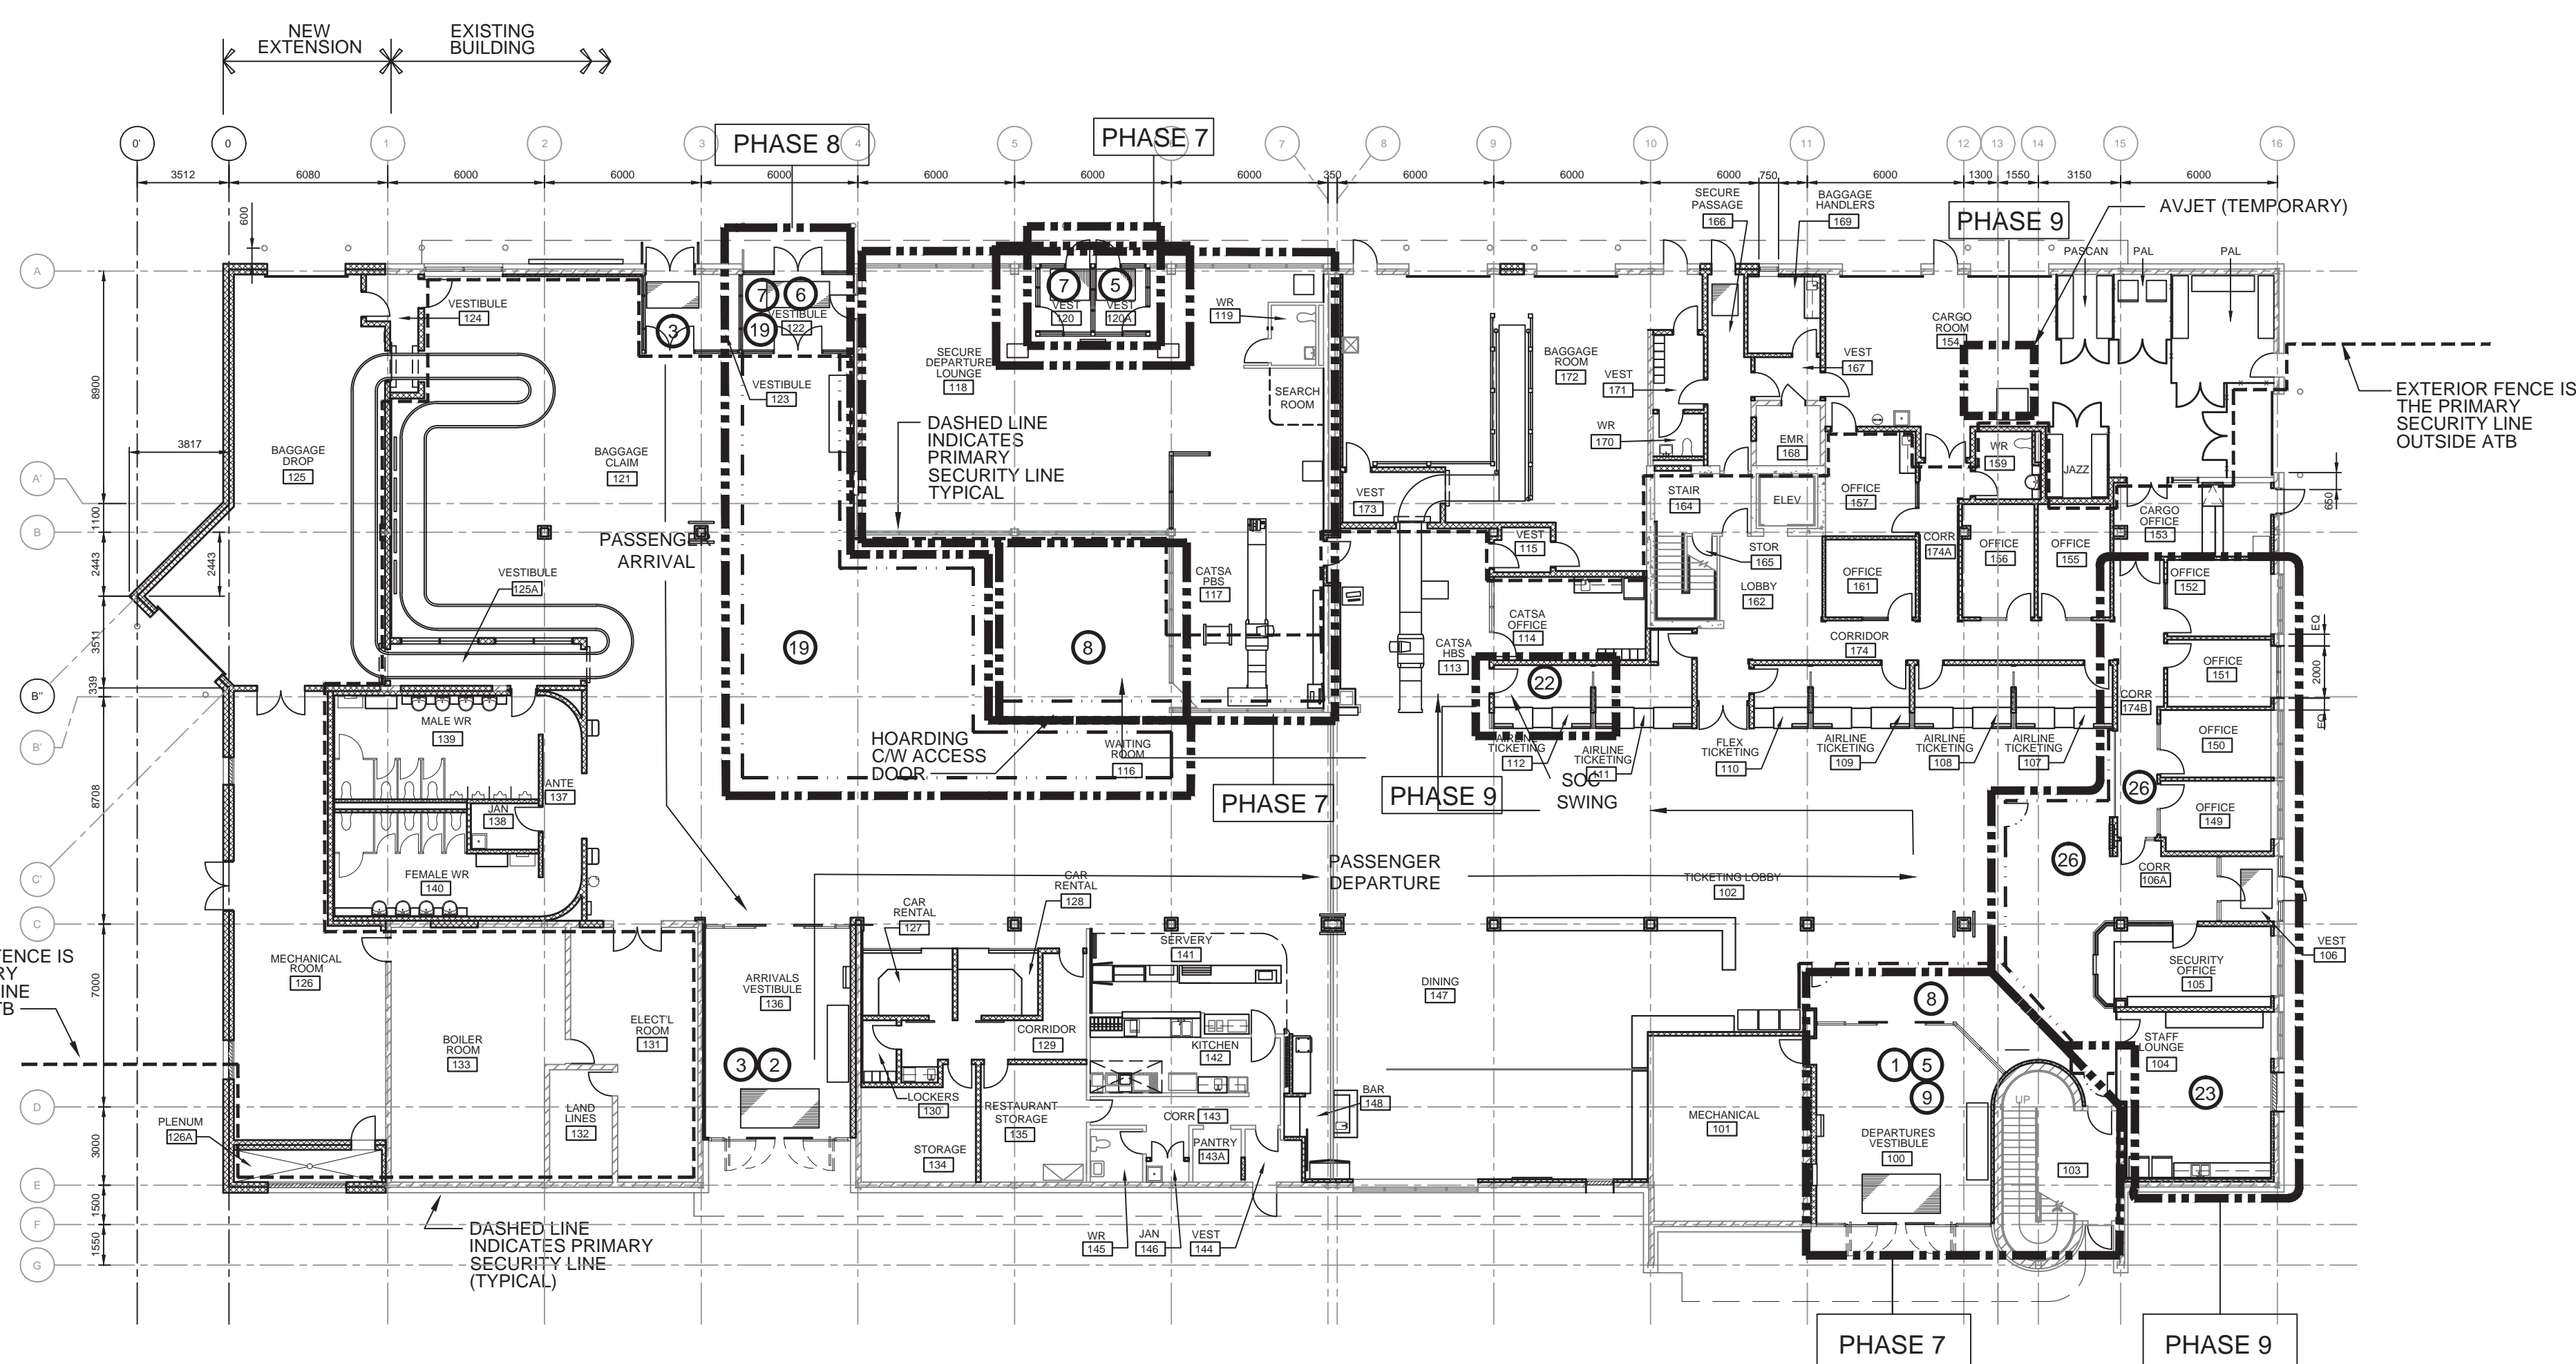

FLOOR PLAN – LEVEL 1 NEW, PHASE 7, 8, 9

2
A-106 | A-106

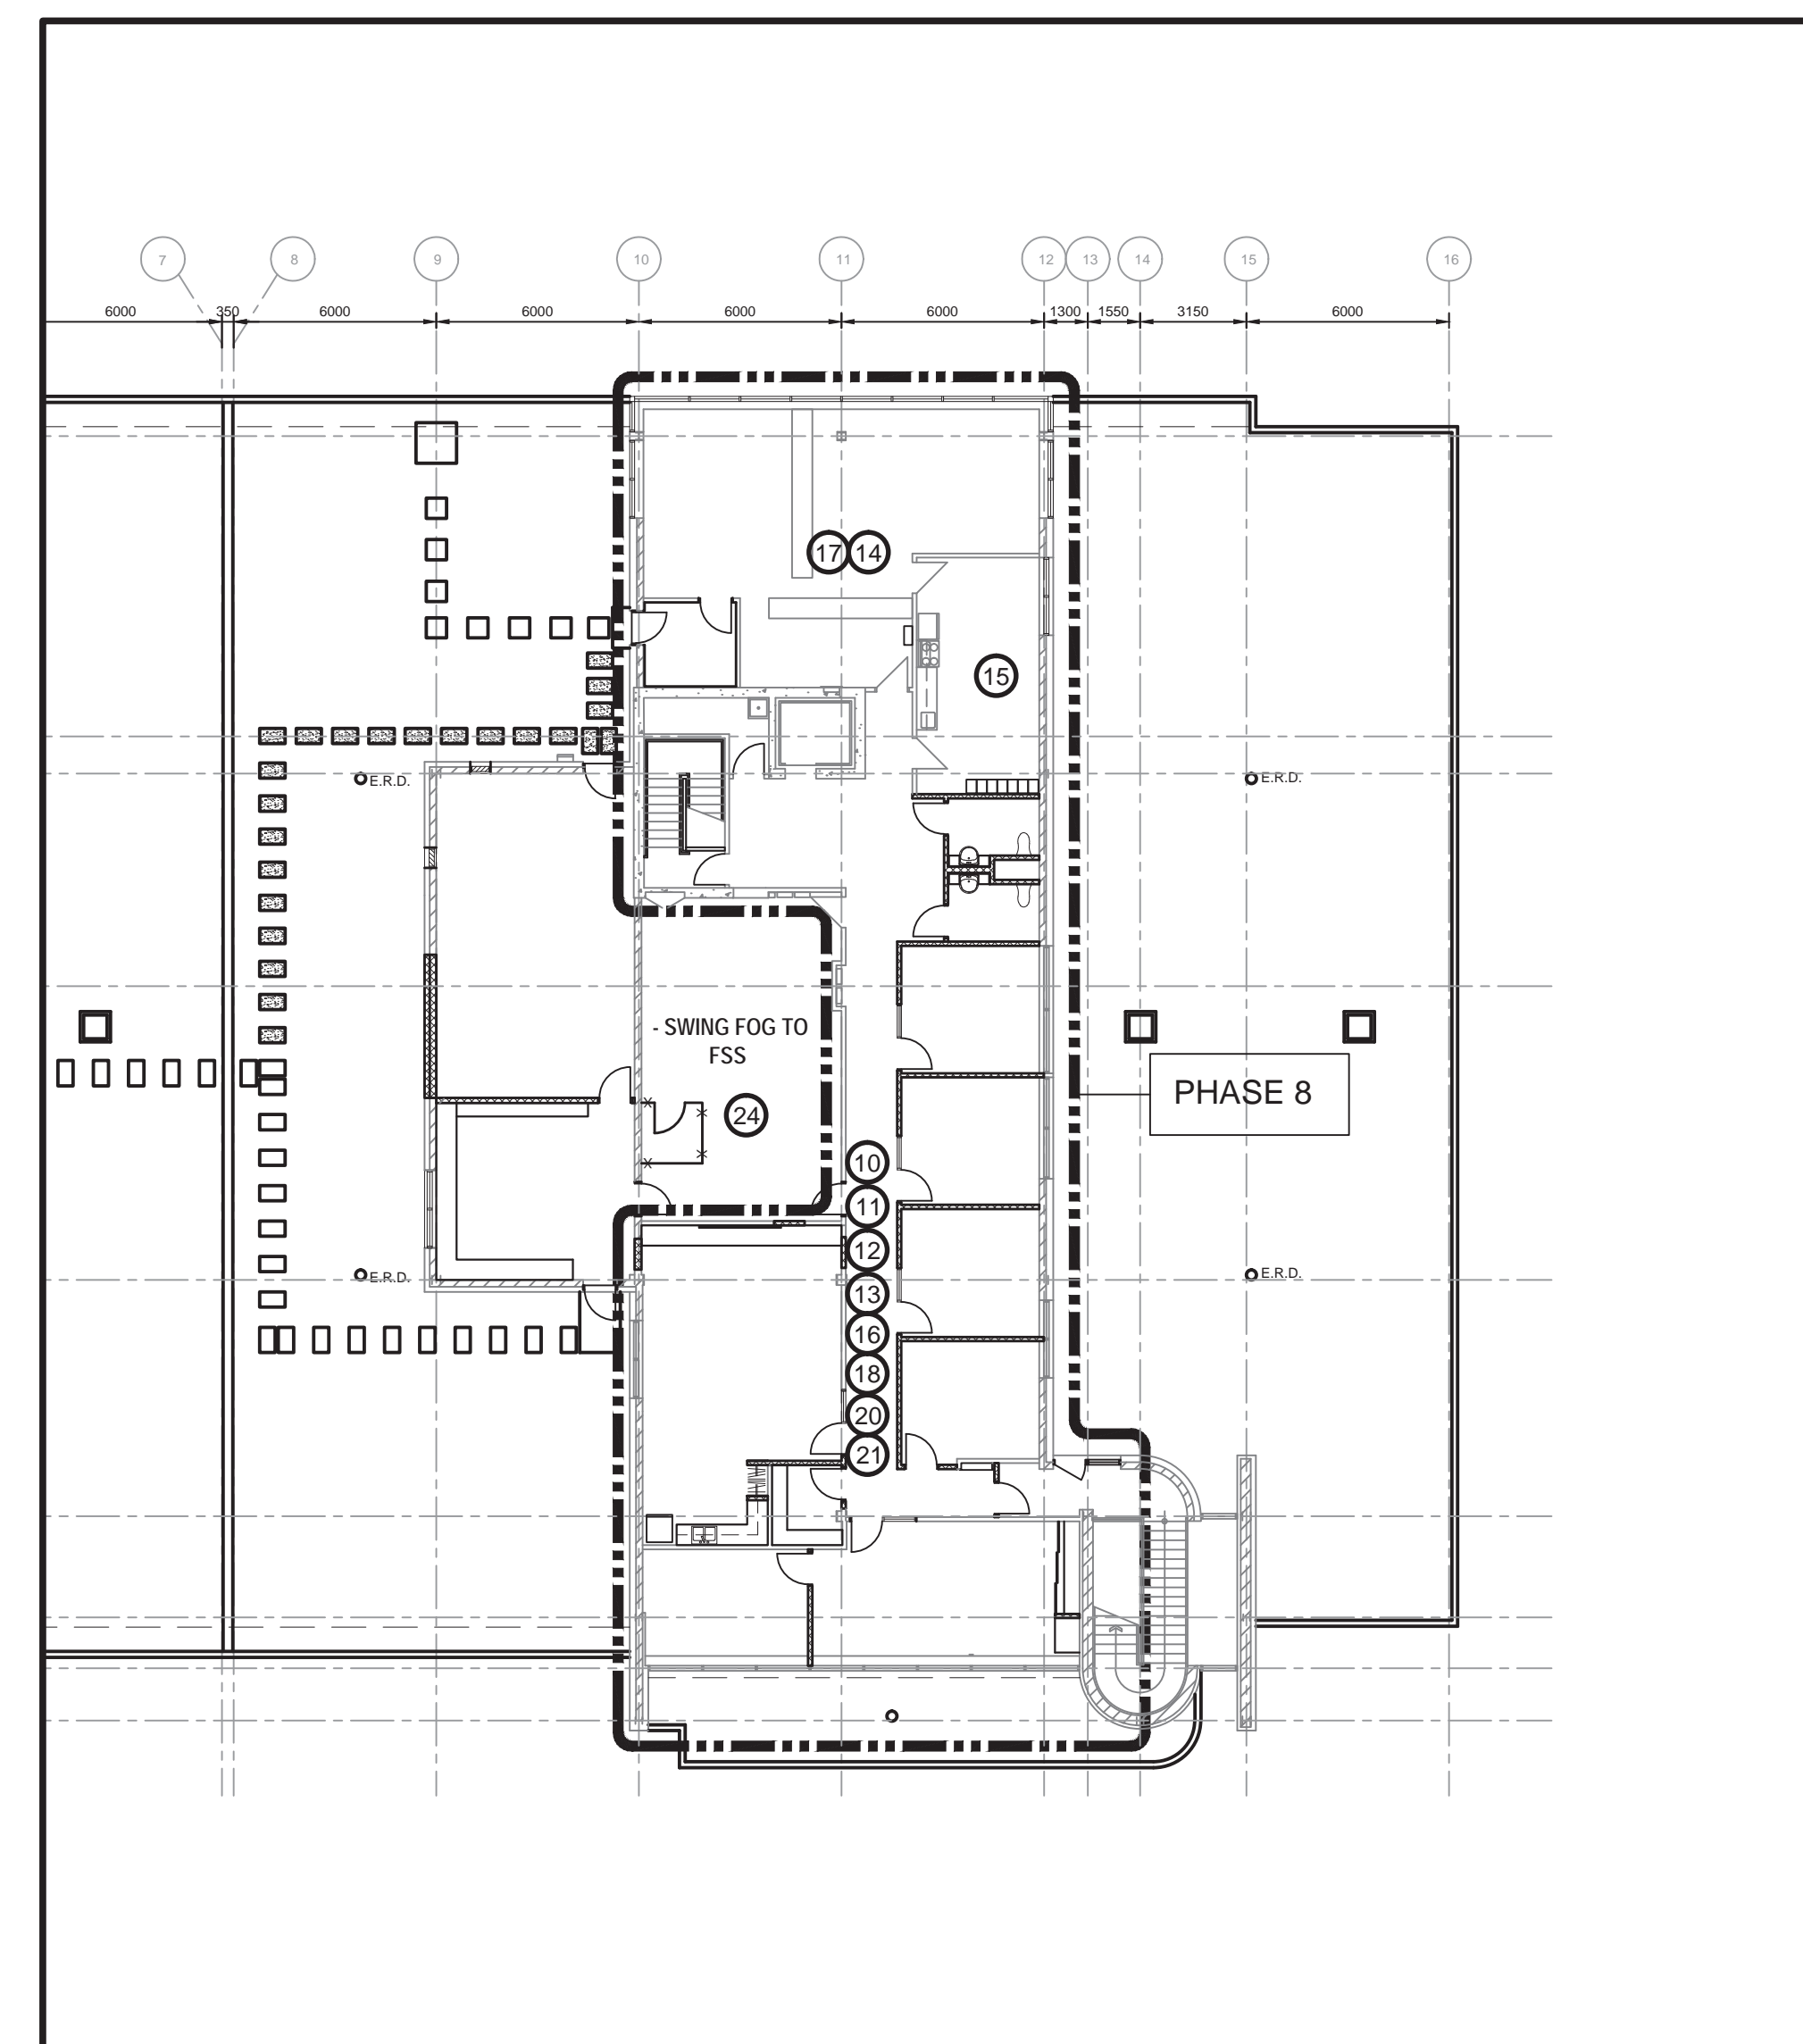

PHASING 7, 8, 9 LEVEL 2 NEW.

3
A-106 | A-106

0	ISSUED FOR TENDER	30/03/2017
revisions		date
project	WABUSH ATB RENOVATION	
	WABUSH AIRPORT	
	WABUSH, NL	
drawing	PHASING PLANS –	
	PHASE 7, 8, 9	
designed	conçu	
drawn	DNF / TB/ RP	dessiné
date	OCT 2016	
approved	approuvé	
date		
Tender	Soumission	
PWSSC Project Manager	Administrateur de projets TPSSC	
project number	no. du projet	
	R.076412.001	
drawing no.	no. du dessin	
	A-106	
