


FLOOR PLAN – LEVEL 1 EXISTING, PHASE 10, 11, 12

SCALE: 1:200

1  
A-107 A-107

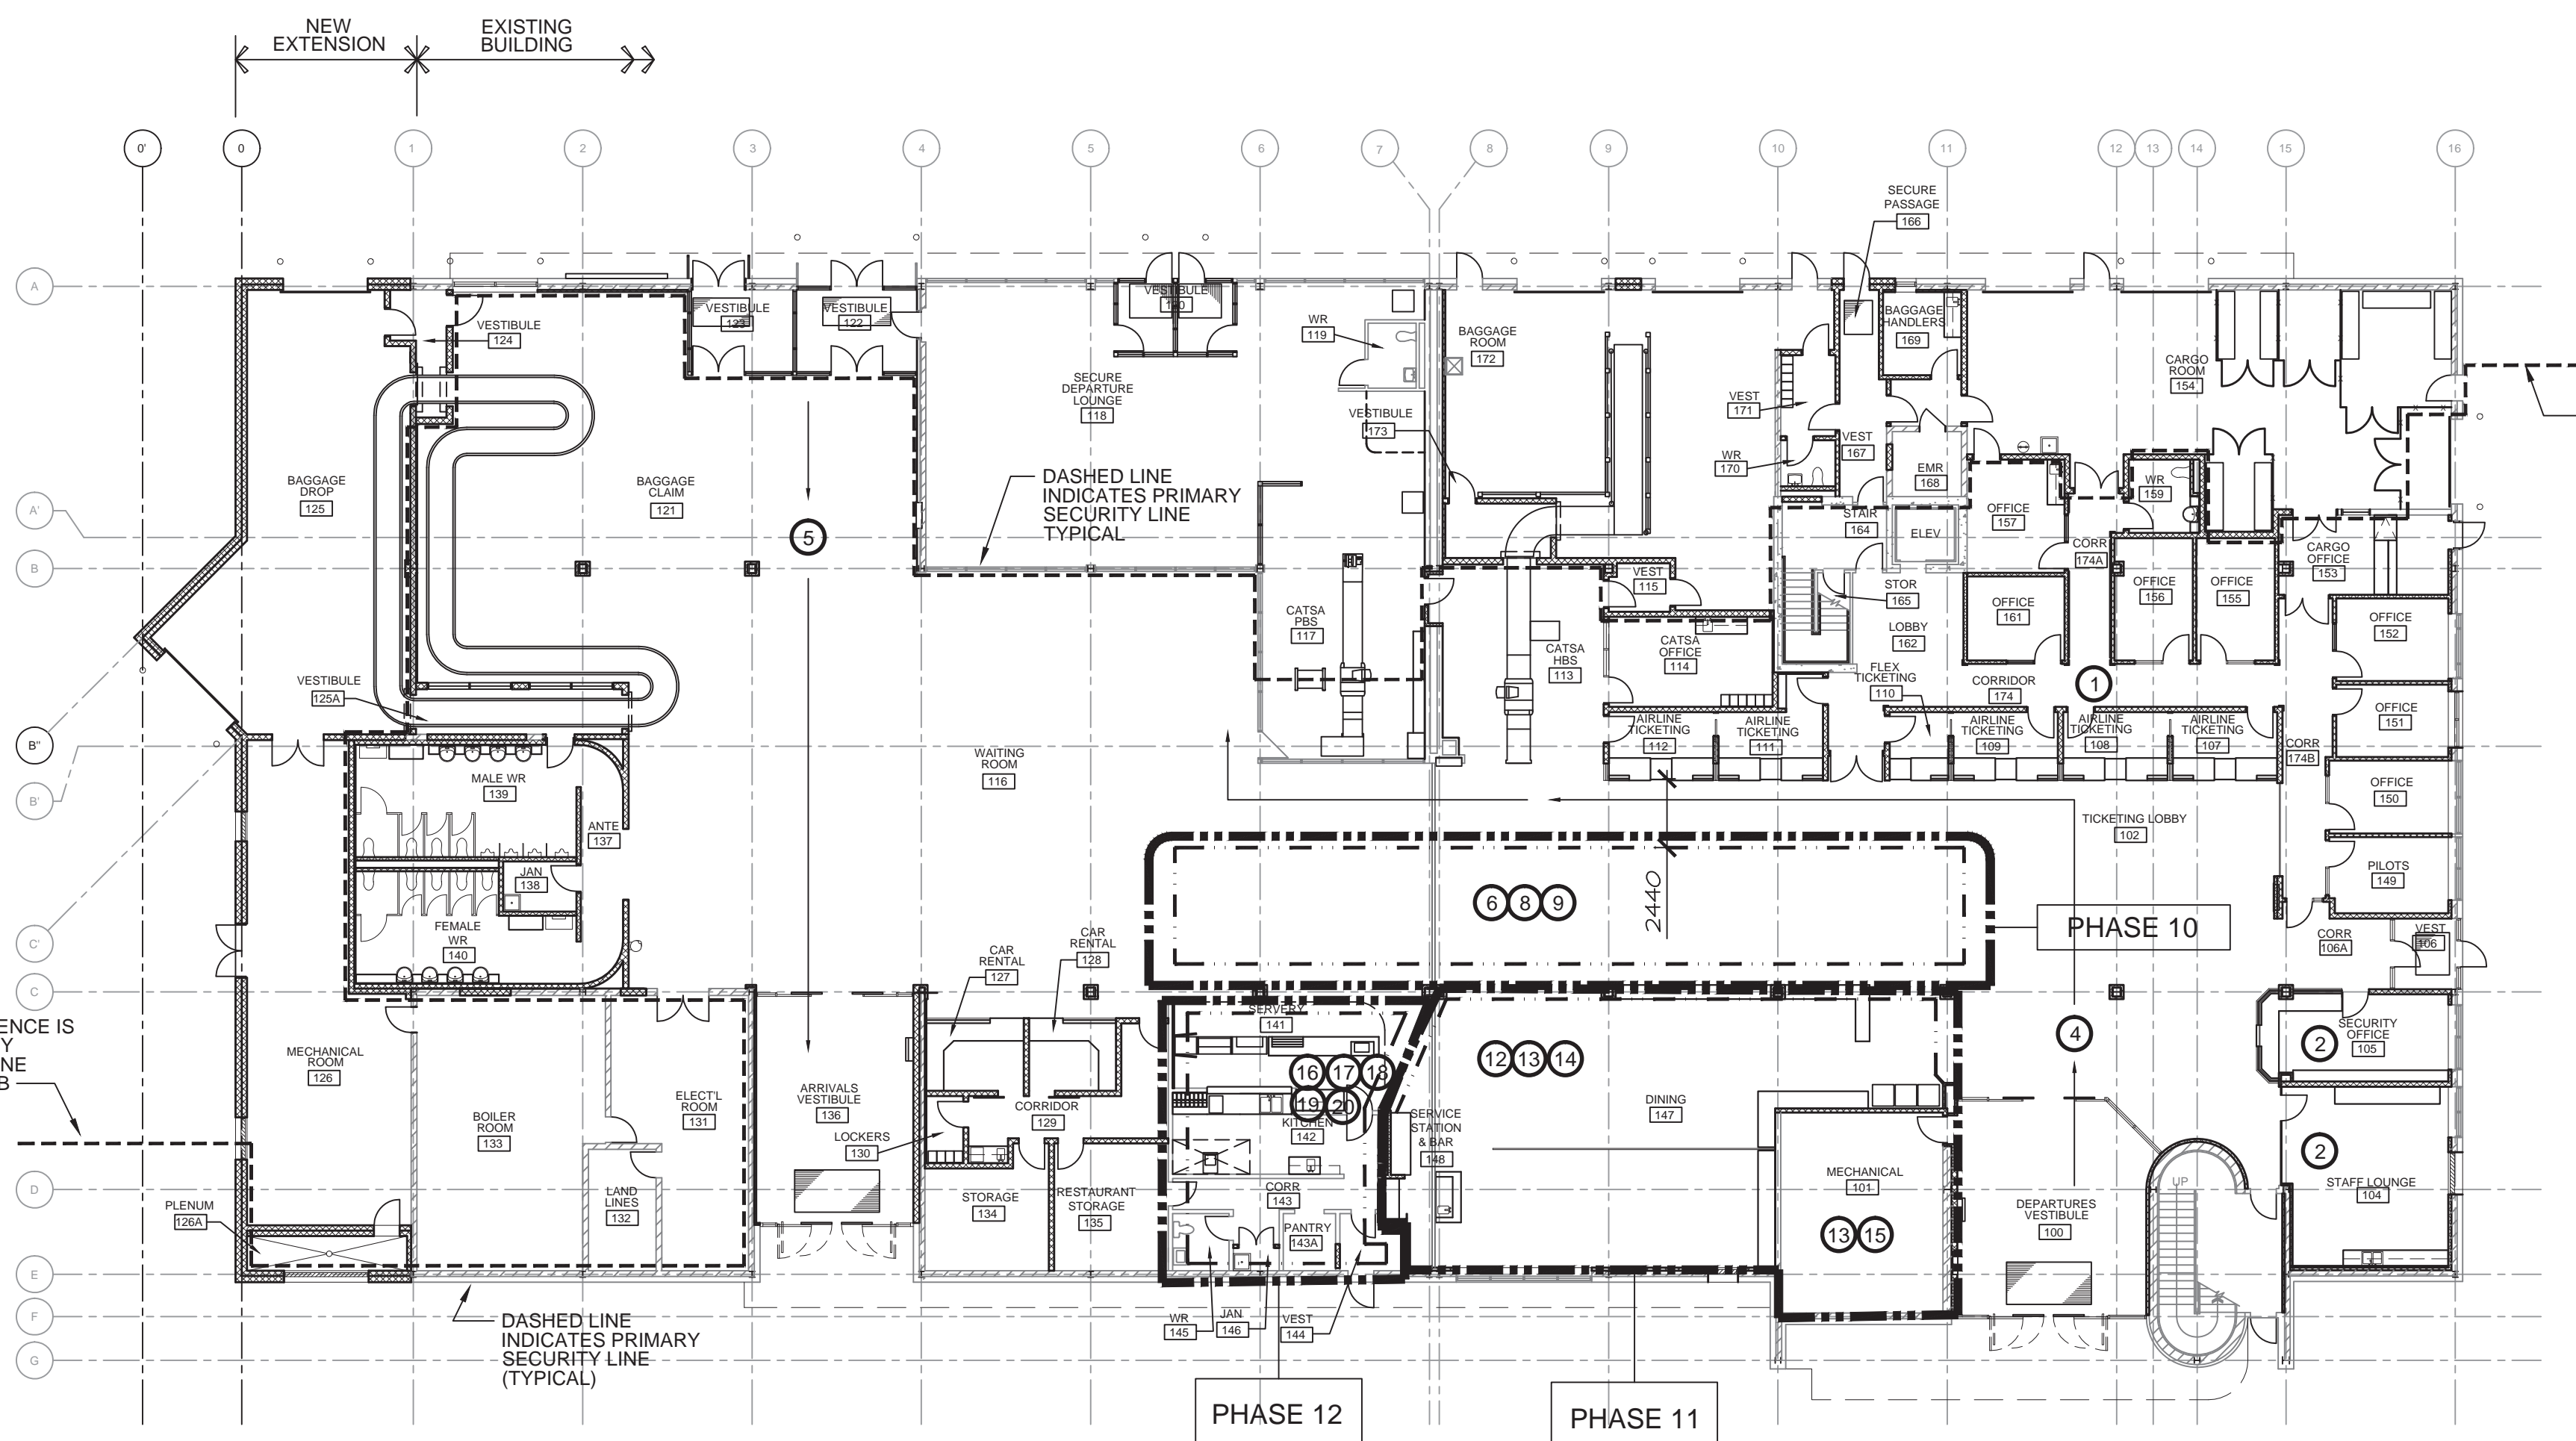

FLOOR PLAN – LEVEL 1 NEW, PHASE 10, 11, 12

SCALE: 1:200

2  
A-107 A-107

## PHASING OBJECTIVES:

PHASE 10 (RENOVATE CENTRAL CONCOURSE AND MECHANICAL ROOM #223, WORKSHOP ROOM #219, EQUIPMENT ROOM #221, SECOND FLOOR):

SCHEDULE: DURATION 2 WEEKS

1. LEVEL 1 NEW TICKETING AND BACK OF HOUSE OFFICES IN OPERATION.
2. LEVEL 1 NEW SECURITY 105 AND MEETING ROOM 104 IN OPERATION.
3. LEVEL 2 NEW TOC AND FSS IN OPERATION.
4. PASSENGER DEPARTURE: PASSENGERS ARRIVE THROUGH NEW DEPARTURES VESTIBULE 100, PROCEED TO NEW TICKETING COUNTERS, DROP BAGGAGE AT NEW CATSA HBS, PROCEED TO CATSA PBS.
5. PASSENGER ARRIVALS: PASSENGERS ARRIVE THROUGH NEW VESTIBULES 122 AND 123, CLAIM BAGGAGE AT NEW BAGGAGE CLAIM 121, PROCEED TO NEW ARRIVALS VESTIBULE 136.
6. SECURE CONSTRUCTION ZONE AND ASBESTOS ABATEMENT.
7. RENOVATE SECOND LEVEL MECHANICAL ROOM #223, WORKSHOP ROOM #219 AND EQUIPMENT ROOM #221.
8. RENOVATE CONCOURSE AREA LOCATED WITHIN PHASE 10 - AREA A (INCL. ARCHITECTURAL, MECHANICAL, ELECTRICAL AND FIRE SUPPRESSION).
9. REOPEN PHASE 10 - AREA CONCOURSE TO PUBLIC.
10. REMOVE EXISTING AHU-1 (SERVING LEVEL 2) AND AHU-2 (SERVING LEVEL 1).
11. INSTALL AND COMMISSION NEW AHU-5 SERVING LEVEL 2 OFFICES

PHASE 11 ( RENOVATE DINING AREA #147 AND MECHANICAL ROOM #101):

SCHEDULE: DURATION 3 WEEKS

12. SECURE CONSTRUCTION ZONE AND ASBESTOS ABATEMENT.
13. RENOVATE DINING AREA #147 AND MECHANICAL ROOM #101, KITCHEN TO REMAIN FUNCTIONAL.
14. TEMPORARILY MOVE SOME TABLES TO CONCOURSE AREA.
15. INSTALL AND COMMISSION NEW AHU-3 (BOH) AND AHU-4 (RESTAURANT) WITH ASSOCIATED DUCTWORK


PHASE 12 (RENOVATE KITCHEN):

SCHEDULE: DURATION 2 WEEKS

16. SECURE CONSTRUCTION ZONE AND ASBESTOS ABATEMENT.
17. PROVIDE TEMP SERVICE FROM NEW BAR AREA.
18. RELOCATE COOLER FOR SANDWICHES ETC.
19. SOUP AND COFFEE TO BE SERVED FROM BAR AREA.
20. POS TEMPORARILY RELOCATED.

PHASE 10, 11, 12 MECHANICAL:


- EXISTING AHU-1 AND AHU-2 TO BE REMOVED.
- NEW AHU-3 (LOCATED IN MECHANICAL 101) TO BE INSTALLED AND COMMISSIONED. TO SERVE LEVEL 1 BACK OF HOUSE OFFICES.
- NEW AHU-4 (LOCATED IN MECHANICAL 101) TO BE INSTALLED AND COMMISSIONED. TO SERVE KITCHEN AND DINING.
- NEW AHU-5 (LOCATED IN MECHANICAL 223) TO BE INSTALLED AND COMMISSIONED. TO SERVE LEVEL 2.
- NEW AHU-1 AND AHU-2 IN FULL OPERATION SERVING CONCOURSE, SECURE DEPARTURE AND BAGGAGE HANDLING.

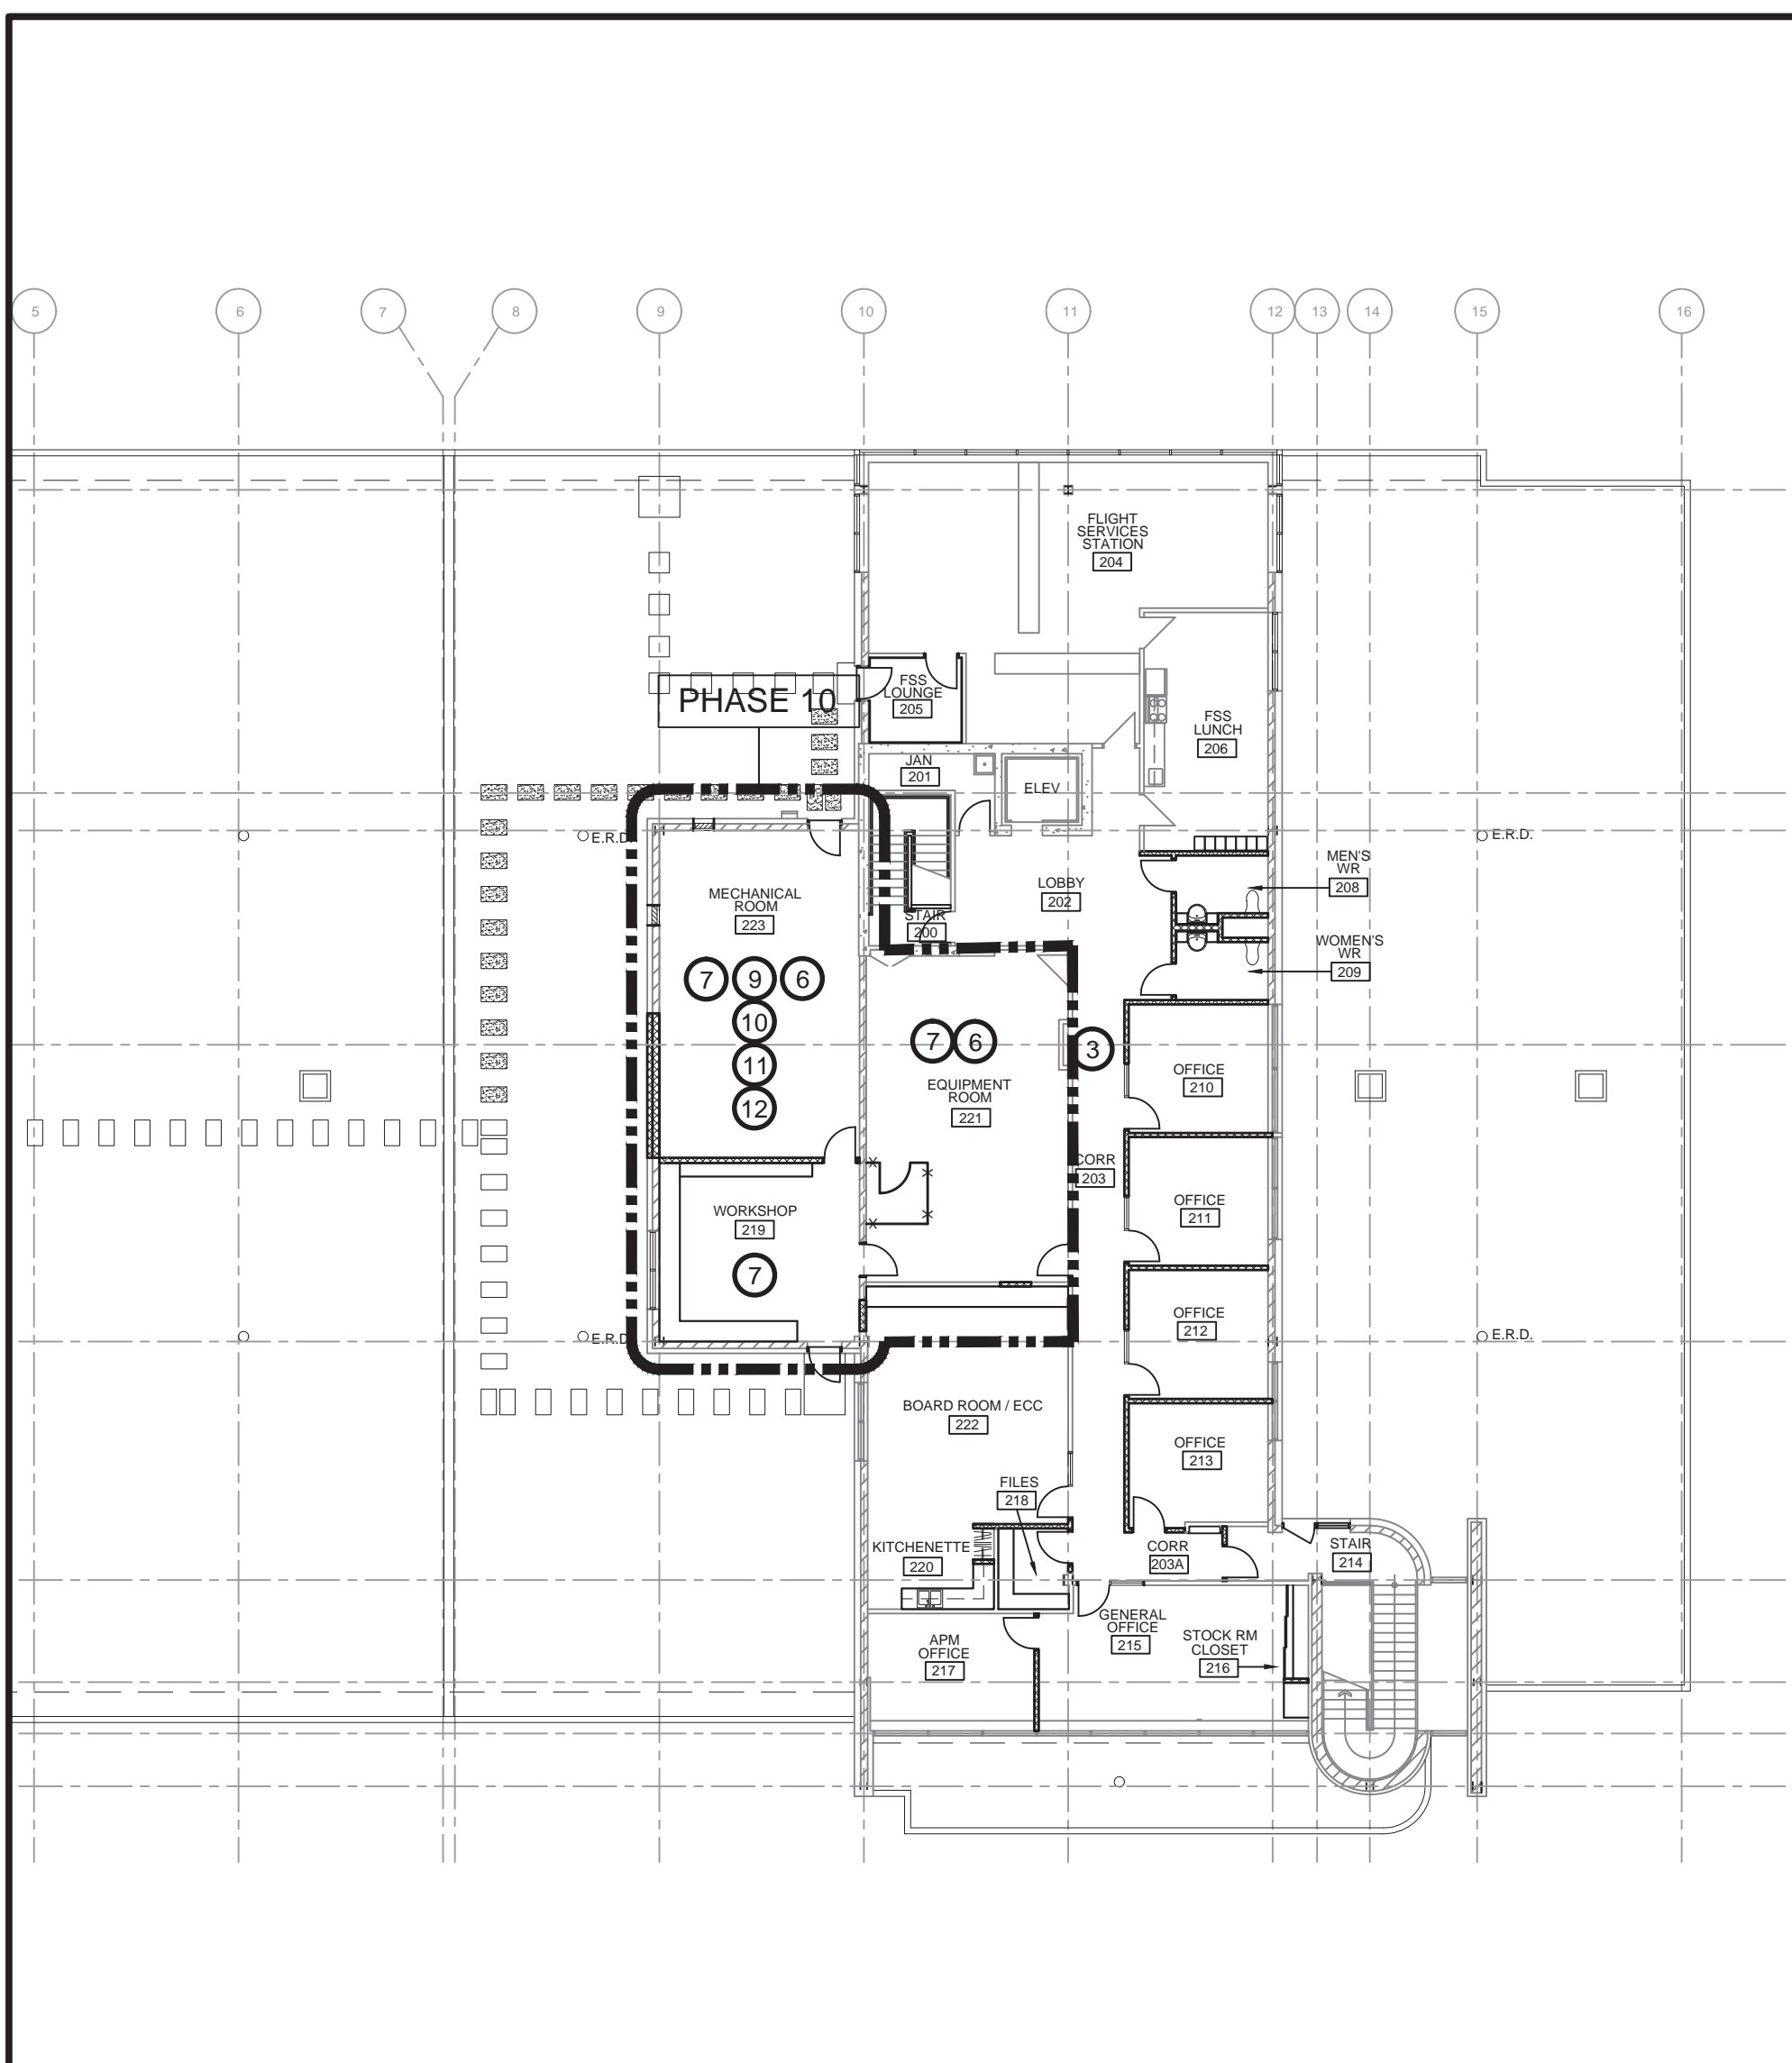

LEVEL 2 NEW, PHASE 10, 11, 12

SCALE: 1:200


3  
A-107 A-107

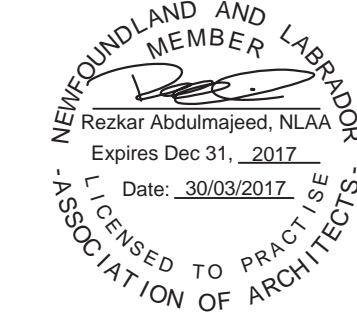

prime consultant:

ARCHITECTURE 49

sub consultant:

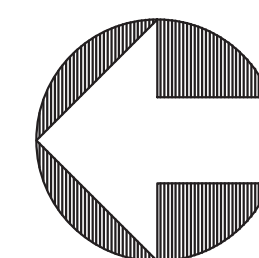

APPROX. NORTH

0 ISSUED FOR TENDER 30/03/2017

revisions date

project WABUSH ATB RENOVATION

WABUSH AIRPORT  
WABUSH, NL

drawing PHASING PLANS –  
PHASE 10,11,12

designed conçu

drawn DNF / RP dessiné

date OCT 2016

approved approuvé

date

Tender Submission

PWSSC Project Manager Administrateur de projets TPSSC

project number no. du projet

R.076412.001

drawing no. no. du dessin

A-107
